

DATE: 08 OCTOBER 2020

REPORT TO: HUMAN SETTLEMENTS PORTFOLIO COMMITTEE

1. ITEM NUMBER: HS 14/10/20

2. SUBJECT

STATUS REPORT ON HUMAN SETTLEMENTS CURRENT AND PLANNED **PROJECTS**

ONDERWERP

STATUSVERSLAG OOR MENSLIKE NEDERSETTINGS SE HUIDIGE EN BEPLANDE **PROJEKTE**

ISIHLOKO

UBUME BENGXELO **EMALUNGA** NEEPROWUJEKTHI ZAKALOKUNJE NEZICWANGCISIWEYO EZINGEZOKUHLALISWA KOLUNTU

3. DELEGATED AUTHORITY

In terms of delegation

This report is FOR NOTING BY

✓ Committee name : Human Settlements Portfolio Committee

☐ The Executive Mayor together with the Mayoral Committee (MAYCO)

☐ Council

4. DISCUSSION

This report provides an overview of all current and planned service delivery projects in the Directorate of Human Settlements for 2020/21 and beyond. The report covers various housing instruments available to the Directorate which includes HSDG, USDG, CRU, Incremental Housing, Social Housing and Emergency Housing.

Making progress possible. Together.

143

Financial Implications	☑ None ☐ Opex ☐ Capex
	☐ Capex: New Projects
	☐ Capex: Existing projects requiring additional funding
	☐ Capex: Existing projects with no additional funding requirements
Policy and Strategy	☐ Yes ☑ No
Legislative Vetting	☐ Yes ☑ No
Legal Compliance	
Ctaff Implications	
Staff Implications	☐ Yes ☑ No
Risk Implications	☐ Yes ☑ No
5. RECOMMENDATIONS	
That the report be noted by the	e Human Settlements Portfolio Committee.
AANBEVELING	
Dat die portefeuljekomitee o	or menslike nedersettings van die verslag kennis neem.
IZINDULULO	
Ukuba iKomiti yeMicimbi en	gokuHlaliswa koLuntu mayiqwalasele ingxelo.
	Making progress possible. Together.

Α	N	N	EX	U	R	ES

Annexure 1.1 Housing Development – Summary of Progress Report on all Projects – 10								
September 2020								
Annexure 1.2	Social Housing – Current and Planned Projects – 10 September 2020							
Annexure 2.1	Informal Settlements Projects Monitoring Report							
Annexure 2.2	Informal Settlements – Current Projects Portfolio – September 2020							
Annexure 2.3	Informal Settlements – Project Portfolio Planning and Pipeline							
Annexure 3	Public Housing Projects – Full Plan							

FOR FURTHER DETAILS CONTACT

NAME	Lawrence Valeta	CONTACT NUMBER 021 400 4525
E-MAIL ADDRESS	Lawrence.Valeta@capetown.gov.za	
DIRECTORATE	HUMAN SETTLEMENTS	FILE REF NO
SIGNATURE : MANAGER SUPPORT SERVICES		

EXECUTIVE DIRECTOR

NAME	Nolwandle Gqiba	(COMMENT:
DATE			
SIGNATURE			

LEGAL COMPLIANCE

☐ REPORT COMPLIANT WITH THE PROVISIONS OF COLLEGISLATION RELATING TO THE MATTER UNDER CONSID	· · · · · · · · · · · · · · · · · · ·
□ NON-COMPLIANT	
NAME	COMMENT:
DATE	
SIGNATURE	

Making progress possible. Together.

Approval Form Supported for inclusion on the agenda



STATUS REPORT ON HUMAN SETTLEMENTS CURRENT AND PLANNED PROJECTS

Report Reference: 515788

Meeting: Section 79 Portfolio Committee - Human Settlements

Meeting Date: 08.10.2020

Meeting Venue: Meeting Room A 5TH Floor Podium

Contact Person: Lawrence Valeta
Contact Telephone: 0214005315

Contact Email: LAWRENCE.VALETA@CAPETOWN.GOV.ZA

Item	Section	Approver	Approval	Approved Date	Approver Comments
01	Author	Lawrence Valeta	Approved	23.09.2020 12:37:12	
02	Director	Nolwandle Gqiba	Approved	23.09.2020 12:42:32	
03	Executive Director	Nolwandle Gqiba	Approved	23.09.2020 12:44:57	
04	Legal Compliance	Joan Mari Holt	Approved with Comments	25.09.2020 12:28:48	For information.
05	Chairperson	BEVERLEY VAN REENEN	Approved	28.09.2020 09:39:19	

ECS Officer: C Minnaar

<u>Human Settlements: Housing Development: Housing Implementation's list of projects - 10 September 2020</u>

No.	Projects in Planning Stage	Potential Units	Area	Region 1,2,3,4	Project Manager	Sub-Council	Ward	Comments on Progress - 10 September 2020
1	Aloe Ridge	1050	Blue Downs	2	Quintus Welman	21	108	Extension of the town planning approval validity has been received. Southern portion - extension validity of Environmental Approval received. Northern portion - Environmental Impact Assessment application for amendment application be submitted shortly. Environmental Offset Discussions with DEAD&P is ongoing to
					Ryan			agree if the botanical species can also be accommodated on Erf 2003. Land Use: Designs are ongoing and various interdepartmental meetings have taken place between the Planners and Transport departments. General: The Mayco member has presented the latest progress
2	Annandale	2.500	Milnerton	1	Thomas	3	1	made at Sub Council 3 on 13 August 2020. The Valuation report to Council recommending sale of the plots to has been delayed due to outstanding Town Planning
3	Atlantis GAP Sites	650	Atlantis	1	Rivaaj Mahabeer	1	32	approvals for the Robinvale and Beaconhill areas. Property Management have been requested to assist with the sale of
4	Atlantis Kanonkop (Ext.12) Phase 2	1.870	Atlantis	1	Rivaaj Mahabeer Grobler	1	29	USDG funding application is complete. Project split into two sub- phases. Phase 2A has all its planning approvals in place for eighteen (18) land parcels yielding 1,160 sites. Detailed design of Civil, Bulk, Electrical services is underway, SDP for landscaping complete. Phase 2B which will require planning, design & implementation of civil- and electrical engineering services for the servicing of 710 new sites. Regional Professional Team appointed and planning and design
5	Belhar Vacant School Sites & surrounding properties	1.300	Belhar	3	Basson	6	12, 22	work has commenced.
6	Blueberry Hill	4.000	Blue Downs	2	Van Jaarsveld Grobler	22	17	Still await the Environmental Authorisation which was delayed because of the COVID lock down period. Following this, a Town Planning approval can be obtained. Land use approval subject to Municipal Planning Tribunal
7	Bonteheuwel Infill	361	Bonteheuwel	3	Basson	5	50	decision of September 2020.
8	Darwin Road Delft Symphony Way Corridor (ACSA) (Site B)	3.657 1.675	Kraaifontein Delft	1	Ryan Thomas Grobler Basson	7	105	The revised Environmental Basic Assessment Report was advertised on 14/08/2020 and a 30-day public participation process will end on 14/09/2020. All comments will then be included in the final revised Basic Assessment Report which will be submitted to the Minister by the end of September 2020. Await Development approval which is subject to the cancellation of a servitude. City and ACSA legal will submit an urgent court application to uplift the servitude.
					Mahier			The Town Planning Application was advertised on 07 August 2020 for the 30 days public participation process.
11	Elsiesriver Infill	761	Grassy Park Elsiesriver	3	Abrahams Neil Williams	18	25,26 & 28	The Town Planning application advertisement has closed for 2 of the sites on 24 July 2020. The closing date for comments on the third site was 24 August 2020 and the public participation comments will close on 28 September 2020 for the fourth site. All comments obtain will be address by the Town Planners. The housing typologies were presented to Project Steering
12	Falsebay	327	Khayelitsha	2	Feziwe Ngquba	10	99	Committee and Ward Councillors. The Councillors will present the proposed house plans to their communities for approval. A meeting has been scheduled with the Planning Department to discuss the submission of plans for approval. A portion of the site was invaded recently.
13	Farm 920 plus Bloubos Road	574	Sir Lowry's Pass	2	Johan Brand	24	84	Final draft layout was prepared based on all specialist studies. Historical heritage and environmental reports are being reviewed. Permits for Land surveyor and Geotech studies to be issued to go on site for studies.
14	Grassy Park	1100	j	4	Jose' Britto			Regional Professional Team has been appointed to prepare a Development Framework on the identified sites.
15	,	2.500	Athlone	3	Neil Williams	11, 17	& 47 48 & 49	Development Framework has been completed. A meeting with Management will be arranged to discuss the recommendations of the report. Approximately 2 500 housing opportunities identified in 2 possible projects
16	Hanover Park	761	Hanover Park	3	Neil Williams	11	47	Revised layouts have been completed - Parks & Recreation and Urban design have given comments. Once all comments have been received from Line Departments the layouts will be finalised for approval by the Project Steering Committee.

Page									
Notabutyo Figure Phase 2 110 Hangberg Phas									,
Noted by Parise 2 10 Hangberg Phase 2 1 Bill 16 7 1 Mitchelf's Plain 2 1 Bighlands Drive Infill 711 Mitchelf's Plain 4 Basson 23 7 5 7 8 2 27 5 7 8 2 2 2 2 2 2 2 2 2									two identified parcels of land is not feasible for development due
17 Hangberg Phase 2 18 Highlands Drive Infili 19 Highlands Drive Infili 19 Kensington 10 Kensington									
17 Hangberg 1 Belli 16 74 have resized. Record Professional Team is proceeding all continos islantial for the infilit 711 Milchell's Plain 4 Beason 25 75, 76 8 Beason						Noluvuyo			
Registration Project Registration Proj	17	Hangberg Phase 2	110	Hangberg	1	,	16	74	
Bernie Golder Bernie Highlands Drive Infili Kenaington 18 Kenaington 19 Kenaington 19 Kenaington 19 Kenaington 10 Belli 20 Khayelisha CBD Housing Development 308 Khayelisha 20 Private 10		Trangoorg Triado E	1.10	riangsorg	 ' -	Didii		· ·	
Highlands Drive Infili Highlands Drive Infili Notice Infili Not									
Highlands Drive Infill						Grobler			
Noluvuyo Billi Sensington 18 Kensington 19 Kinyelisha CBD Housing Development and senders in the self-state of the body on the self-state of the body of t	18	Highlands Drive Infill	711	Mitchell's Plain	4	Basson	23	75, 76	• •
Note									The Regional Professional Team is undertaking planning and
15 Kensington 168 Kensington 175 Bill 15 Bill									design for the two identified parcels of land in order to obtain
16 Kenangton 168 Kenangton 17 Bidd 15 56 Section Community be an advantage of Stranger Communities has been advantage assessing for Stranger Communities has been advantaged assessing for Stranger Communities has been advantaged assessing for Stranger Communities has been advantaged assessing for Stranger Communities and Stranger Communities has been advantaged as assessment from the problem of the Bernard Register of the Stranger Communities and assessment from the problem of the Stranger Communities and assessment from the Stranger Communities and Strang						Moluvuvo			development & funding approvals. Other land is being sought in
Search S	40		400		١,	,	4-	50	
20 Khayelisha CBD Housing Development 368 Khayelisha 2 Private 10 9 document of the control of t	19	Kensington	168	Kensington	1	Bidii	15	56	
Standard CRD Housing Development 388 Khayelilaha 2 Private 10 3 4 4 5 5 5 5 5 5 5 5									
Transport for Observation to undertake on assessment for developed process and process has been administed to the Regional Professional growth as been administed to the Regional Professional Growth process and purposes has been administed to the Regional Professional Growth passed and process that been administed to the Regional Professional Growth and and provide the Control of the STR. Moreover and the Control of the	20	Khayelisha CRD Housing Development	369	Khaveliteha	2	Drivate	10	0.4	
dovolop ability of 2 isomittinal lead protection and protection for in the Regional Professional Team to provide a support and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provide the City with a clear 1 provided and provided the City with a clear 1 provided and provided the City with a clear 1 provided and provided the City with a clear 1 provided and provided the City with a clear 1 provided and pro	20	Khayelisha CBD Housing Development	300	Kilayelilsila	-	riivale	10	94	
be Regional Professional Learn to provide a quotiento for under Macassar and Earn of provide a depailing season of Earn of 24 Macassar and Earn of the State of State (Macassar) and Earn of Earn									
Langa Phase 2 - Special Quarters 4.04 Langa 1 Abrahams 15 5 South Results of the South Result									
21 Kramat Project 22 Kramat Project 23 Kramat Project 24 Langa Phase 2 - Special Quarters 25 Langa Phase 2 - Special Quarters 26 Langa Phase 2 - Special Quarters 27 Langa Phase 2 - Special Quarters 28 Langa Phase 2 - Special Quarters 29 Langa Phase 2 - Special Quarters 29 Langa Phase 2 - New Flats 20 Langa Phase 2 - New Flats 20 Langa Phase 2 - Special Quarters 20 Langa Phase 2 - Special Quarters 20 Langa Phase 2 - Special Quarters 21 Langa Phase 2 - New Flats 22 Langa Phase 2 - New Flats 23 Langa Phase 2 - Special Quarters 24 Langa Phase 2 - New Flats 25 Langa 1 Abrahams 25 Langa 1 Abrahams 26 Social Housing Regulatory Authority (SHA) to request them to export the revertible of the report to the special Regulatory Authority (SHA) to request them to export the revertible of the report to the special Regulatory Authority (SHA) to request them to export the revertible of the report to the special Regulatory Authority (SHA) to request them to export the revertible of the report to the special Regulatory Authority (SHA) to request them to export the revertible of the report to export the revertible of the revertible of the report to export the revertible of the report to export the revertible of the revertible of the report to export the revertible of the									
Abrahams Community Resident Community Residen									
Development Farmework that would inform the next phase of the population of the control of the									
be determined determin									Development Framework that would inform the next phase of the
Accessor			to be			Olwothu			·
Ramat Project Getermined Macassar 2 Nikime 24 109 Moor, (IPV), with he leaved Mooring Diversionpherm has disabled at report to be supported in the footing Diversionpherm has disabled at report to be supported in the footing Diversion and the state of the composition of the compos	0.4	Kramat Drainat		Maaa	_	_		400	
22 Langa Phase 2 - Special Quarters 404 Langa 1 Abrahams 15 Social Housing Regulatory Authority, (SHRA) to request them to support the new Community Rental Links projects as funding from Human Settlements is no longer available. The report is being finalized and will be sent to the SHRA by the end of Social Housing Regulatory Authority, (SHRA) to request them to support the new Community Rental Links projects as funding from Human Settlements is no longer available. The report is social Housing Regulatory Authority, (SHRA) to request them to support the new Community Rental Links projects as funding not human Settlements is no longer available. The report is social Housing Regulatory Authority, (SHRA) to request them to support the new Community Rental Links projects as funding not human Settlements is no longer available. The report is social Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Links projects as funding not human Settlements is no longer available. The report is social Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Links projects as funding not human Settlements is no longer available. The report is social Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Links projects as funding in human Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlement Settlements in the SHRA by the end of Settlement Settlements in the SHRA by the end of Settlement Settlement Settlements in the SHRA by the end of Settlement Settlement Settlements in the SHRA by the end of Settlement Settlement Settlements in the SH	21	Kramat Project	determined	Macassar	2	Nkume	24	109	Work (IPW) will be issued
Rushdi 22 Langa Phase 2 - Special Quarters 404 Langa 1 Abrahams 15 55 Rushdi 23 Langa Phase 2 - New Flats 25 Langa 26 Langa Phase 2 - New Flats 27 Langa Phase 2 - New Flats 28 Langa Phase 2 - New Flats 28 Langa Phase 2 - New Flats 29 Langa Phase 2 - New Flats 20 Langa 20 Langa 21 Abrahams 22 Langa Phase 2 - New Flats 20 Langa 21 Abrahams 22 Langa Phase 2 - New Flats 24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 26 Mahama Infill : Harare 27 Docan View Infill 28 Pelican Park Phase 2 29 Pelican Park Phase 2 20 Retreat 20 Retreat 20 Retreat 20 Retreat 20 Strand 21 Johan Brand 22 Johan Brand 23 Strand 24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 2 Langa Phase 2 - Siyahlala 26 Nooiensfontein 27 Ocean View Infill 28 Pelican Park Phase 2 29 Pelican Park Phase 2 20 Strand 20 Langa 20 Langa 21 Johan Brand 22 Johan Brand 23 Strand 21 Johan Brand 22 Johan Brand 23 Strand 24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 2 Langa Phase 2 - Siyahlala 26 Nooiensfontein 2 Langa Phase 2 - Siyahlala 20 Langa 20 Langa 21 Johan Brand 22 Mahama Infill : Harare 2 Langa Phase 2 - Siyahlala 23 Langa Phase 2 - Siyahlala 24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 2 Langa Phase 2 - Siyahlala 26 Nooiensfontein 2 Langa Phase 2 - Siyahlala 2 Langa Phase 2 - Siyahlala 2 Langa Phase 2 - Siyahlala 3 Siyahla S									
22 Langa Phase 2 - Special Quarters 404 Langa 1 Rushdi Rushdi 2 Rushdi 2 Langa Phase 2 - New Flats 3 Langa Phase 2 - New Flats 4 Langa Phase 2 - New Flats 4 Langa Phase 2 - Siyahlala 4 Langa Phase 2 - Siyahlala 5 Langa 4 Langa Phase 2 - Siyahlala 5 Langa 6 Langa 6 Langa Phase 2 - New Flats 6 Langa Phase 2 - New Flats 6 Langa Phase 2 - Siyahlala 5 Langa Phase 2 - Siyahlala 5 Langa Phase 2 - Siyahlala 5 Langa 6 Langa Phase 2 - Siyahlala 6 Langa Phase 2 - Siyahlala 6 Langa Phase 2 - Siyahlala 7 Langa Phase 2 - Siyahlala 7 Langa Phase 2 - Siyahlala 8 Langa Phase 2 - Siyahlala 8 Langa Phase 2 - Siyahlala 9 Langa Phase 2 - S									
22 Langa Phase 2 - Special Quarters 404 Langa 1 Abrahams 15 5 Special Countries 202 Search (1997) Althority (1914A) to request them to social Housing Development has draited a report to be sent to the SHRA by the end of Search (1997) Althority (1914A) to request them to from Human Settlements is no longer available. The report is being final and and will be sent to the SHRA by the end of Search (1997) Althority (1914A) to request them to from Human Settlements is no longer available. The report is being final and will be sent to the SHRA by the end of Search (1997) Althority (1914A) to request them to from Human Settlements is no longer available. The report is being final and will be sent to the SHRA by the end of Search Housing Regulatory Authority (1914RA) to request them to the Shranger of the Search (1997) Althority (1914RA) to request them to support the new Community Replaced and will be sent to the SHRA by the end of Search Housing Regulatory Authority (1914RA) to request them to support the new Community Replaced and will be sent to the SHRA by the end of Search Housing Regulatory Authority (1914RA) to request them to the Shranger of the Search (1914) Althority (1914RA) to request them to support the new Community Replaced and will be sent to the SHRA by the end of Search Housing Regulatory Authority (1914RA) to request them to support the new Community Replaced and will be sent to the SHRA by the end of Search Housing Regulatory Authority (1914RA) to request them to support the new Community Replaced and submitted to the Shranger and the Search (1914) Althority (1914)									
22 Langa Phase 2 - Special Quarters 404 Langa Abrahams 15 51 Sectember 2200. Housing Development has drafted a report to be sent to the Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retail Units projects as funding from Numan Settlements is no longer available. The report is continuously and the sent to the Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retail Units projects as funding from Numan Settlements is no longer available. The report is social Housing Development has drafted a report to be sent to the Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retail Units projects as funding from Numan Settlements is no longer available. The report is social Housing Development has drafted a report to be sent to the Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retail Units projects as funding from Numan Settlements is no longer available. The report is social Housing Development has drafted a report to be sent to the Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retail Units projects as funding from Numan Settlements is no longer available. The report is been from the funding Development of the Section of Section 19 and the support the new Community Retail Units projects as funding from Numan Settlements in so longer available. The report is the Social Housing Development High Section 19 and the Section						Rushdi			
Rushdi 23 Langa Phase 2 - New Flats 25 Langa 1 Abrahams 15 5 Sember 2 - New Flats 25 Langa 1 Abrahams 16 5 Social Housing Regulatory Authority (FHRA) to request them to support the new Community Rental Links projects as funding from Human Settlements is no longer available. The report is being finalised and will be sent to the Series of the sent of the Series of the Social Housing Regulatory Authority (FHRA) to request them to support the new Community Rental Links projects as funding from Human Settlements is no longer available. The report is being finalised and will be sent to the SHRA by the end of September 2020. 24 Langa Phase 2 - Siyahlala 200 Langa 1 Abrahams 15 5 1 Sember 2020. 25 Mahama Infill : Harare 2 200 Khayelitsha 2 Nguba 2 Nguba 3 Nguba 3 Nguba 4 Nooiensfontein 2 200 Blue Downs 2 Quintus 3 Velman 2 Quintus 4 Jose' Britto 4 Jose' Britto 5 Nooiensfontein 2 200 Blue Downs 2 Velman 2 1 Preference of the Strand 3 Strand Erf 5113 4 800 Strand 2 Johan Brand 5 Social Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Links projects as funding from Human Settlements is no longer available. The report is being registed as will be sent to the SHRA by the end of September 2020. 5 Social Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Links projects as funding form Human Settlements in so longer sent sent sent sent sent sent sent sent	22	Langa Phase 2 - Special Quarters	404	Langa	1	Abrahams	15	51	
23 Langa Phase 2 - New Flats 25 Langa 1 Abrahams 15 5 Seclate Housing Regulatory Authority (SHRA) to request them to support the new Community Rental Lulis projects as funding from Human Settlements is no longer available. The report is been to the SHRA by the end of September 2020. Rushdi 24 Langa Phase 2 - Siyahlala 20 Langa 1 Abrahams 15 5 September 2020. Rushdi 24 Langa Phase 2 - Siyahlala 25 Mahama Infill: Harare 2 - 200 Khayelitsha 2 Nojeuba 2 Nojeuba 2 Nojeuba 2 Nojeuba 3 Nooiensfontein 2 - 200 Khayelitsha 2 Nojeuba 2 Nojeuba 3 Nooiensfontein 2 - 200 Khayelitsha 2 Nojeuba 3 Nooiensfontein 2 - 200 Khayelitsha 3 Nooiensfontein 3 Nooiensfontein 3 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 3 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 5 Nooiensfontein 5 Nooiensfontein 5 Nooiensfontein 5 Nooiensfontein 5 Nooiensfontein 6 Nooiensfontein 6 Nooiensfontein 6 Nooiensfontein 7 Ocean View Infill 7 Ocean View Infill 7 Ocean View Infill 7 Ocean View Infill 8 Pelican Park Phase 2 1 .900 Pelican Park 8 Abrahams 1 Nooiensfontein 8 Nooiensfontein 9 Pelican Park 9 Pelican Park 1 Nooiensfontein 1 Nooiensfontein 1 Nooiensfontein 1 Nooiensfontein 2 Nooiensfontein 2 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Jose' Britto 1 Nooiensfontein 1 Nooiensfontein 2 Nooiensfontein 3 Nooiensfontein 4 Nooiensfontein 5 Nooiensfontein 6 Nooi		Langa i nace E opeoidi Quantere		Langa	† ·	7 10 10 11 10 11 10			Housing Development has drafted a report to be sent to the
Langa Phase 2 - New Flats 255 Langa 1 Abrahams 15 51 Seglember 2202. Housing Development has drafted a report to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to be sent to the SHRA by the end of support the new Community Retail Units projects as funding to the support the new Community Retail Units projects as funding to the support the new Community Retail Units project as funding to the support the new Community Retail Units projects as funding to the support the new Community Retail Units projects as funding to the support the new Community Retail Units projects as funding to the new Community Retail Units projects as funding to the new Community Retail Units projects as funding to the support the new Community Retail Units projects as funding to the new Community Retail Units projects as funding to the support to the suppo									
23 Langa Phase 2 - New Flats 25 Langa 1 Abrahams 15 5 September 2020. Rushdi Rushdi Rushdi Rushdi Rushdi Abrahams 15 5 September 2020. Rushdi Rush									
23 Langa Phase 2 - New Flats 25 Langa 1 Abrahams 26 Langa 27 Langa Phase 2 - New Flats 28 Langa Phase 2 - New Flats 29 Langa Phase 2 - Siyahlala 200 Langa 1 Abrahams 201 Langa 202 Langa 203 Langa Phase 2 - Siyahlala 204 Langa Phase 2 - Siyahlala 205 Langa 206 Langa 207 Langa 208 Rayelitsha 208 Retreat 208 Retreat 209 Retreat 209 Pelican Park 209 Pelican Park 209 Pelican Park 209 Retreat 209 Retreat 200 Ret									• • • • • • • • • • • • • • • • • • • •
Langa Phase 2 - New Flats 255									being finalised and will be sent to the SHRA by the end of
Langa Phase 2 - Siyahlala 200 Langa 1 Abrahams 15 Social Housing Regulatory Authority (SHRA) to request them to support the new Community Retal Lultis projects as funding from Human Settlements is no longer available. The report is being finalised and will be sent to the SHRA by the end of Steptember 2020. 25 Mahama Infill: Harare 2.200 Khayelitsha 2 Nociensfontein 2.200 Blue Downs 2 Welman 2 Ocean View Infill 397 Ocean View 2 Nociens Park 2 Pelican Park Phase 2 397 Ocean View 397 Ocean View 398 Pelican Park Phase 2 398 Pelican Park Phase 2 399 Pelican Park 399 Pelican Park 4 Abrahams 200 Retreat 4 Carolus 390 Retreat 4 Carolus 390 Strand 390 St	23	Langa Phase 2 - New Flats	255	Langa	1	Abrahams	15	51	September 2020.
24 Langa Phase 2 - Siyahlala 20 Langa 1 Rushdi Abrahams 15 51 Rushdi Abrahams 15 51 Feziwe Sperimer 2020. The project consists of 8 sites. Town Planning approval for 4 sites have been invaled recently. 25 Mahama Infill : Harare 2.200 Khayelitsha 2 Nooiensfontein 2.000 Blue Downs 2 Welman 21 1 Distriction to Perform Work was issued to the Regional Professional Team with the emaining 4. Abrahams 26 Nooiensfontein 27 Ocean View Infill 387 Ocean View 4 Jose' Britto 4 Jose' Britto 57 Abrahams 18 Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the partment of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Study (Serial Ste									
24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 2 - 2.200 Khayelitsha 2 - 2.200 Blue Downs 2 - 2.200 Welman 2 - 2.200 Welman 2 - 2.200 Blue Downs 2 - 2.200 Welman 2 - 2.200 Welman 2 - 2.200 Blue Downs 2 - 2.200 Welman 2 - 2.200 Welman 2 - 2.200 Welman 2 - 2.200 Welman 2 - 2.200 Blue Downs 2 - 2.200 Welman 2 - 2.200 Welma									
Auga Phase 2 - Siyahlala 200 Langa 1 Abrahams 15 51 September 2020. The project consists of 3 sites. Town Planning approval for 4 sites have been obtained. It is anticipated that the remaining 4 sites will obtain Town Planning approval for 4 sites have been obtained. It is anticipated that the remaining 4 sites will obtain Town Planning approval during October 2020. Quintus 2000 Blue Downs 2 Welman 21 19 Professional Team or 3 Jul 2020. The Professional									
24 Langa Phase 2 - Siyahlala 25 Mahama Infill : Harare 2 2 200 Khayelitsha 2 Nooiensfontein 2 2 Nooiensfontein 2 2 Nooiensfontein 2 2 Nooiensfontein 2 3 Ocean View Infill 3 3 Ocean View Infill 3 3 Ocean View 4 Jose' Britto 4 Abrahams 1 8 The Final Scoping Report (FSR) for the Environmental Affairs and Development Planning approval with conditions have been opposed to the major and and award town in period of 29 days before a Carolus 2 Retreat 5 00 Retreat 4 Carolus 5 1 Strand Erf 5113 4 800 Strand 2 Jaarsveld 8 Bernie 4 Abrahams 1 5 5 Supplember 2220. The project consists of 8 sites. Town Planning approval for 4 sites have been obtained. It is anticipated that the remaining 4 sites will obtain Town Planning approval of the Regional Potential Centry 1 of the 8 sites have been lotalanded recently. The final struction to Perform Work was issued to the Regional Professional Team on 23 Jul 2020. The Professional team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for obtaining Town Planning approval on the Regional Professional Team will be responsible for the Planning approval on the Regional Professional Team will be responsible for the Planning approval on the Regional Professional Team will be responsible for ob						Rushdi			
Second Park Phase 2 Second Park Park Phase 2 Second Park Park Park Phase 2 Second Park Park Phase 2 Second Park Phase 2 Second Park Phase 2 Second Park Park Park Park Park Park Park Park	24	Langa Phase 2 - Siyahlala	200	Langa	1		15	51	
Section Sect		Langa i mase z - oryaniala	200	Langa	+ '-	7 Ibrahamo	10	- 01	
25 Mahama Infill : Harare 2 Ngquba 2 Ngquba 30, 24 94 98 sites will lobain Town Planning approval during October 2020. Ngquba 30 Ngelman									
Zeb Mahama Infill : Harare						Feziwe			sites will obtain Town Planning approval during October 2020.
26 Nooiensfontein 2.000 Blue Downs 2 Quintus Welman 21 Yelman 21 Yelman 21 Yelman 22 Yelman 23 Yelman 22 Yelman 24 Yelman 25 Yelman 25 Yelman 25 Yelman 26 Yelman 27 Yelman 27 Yelman 28 Yelman 28 Yelman 28 Yelman 28 Yelman 29 Yelman 29 Yelman 29 Yelman 29 Yelman 20 Y	25	Mahama Infill : Harare	2.200	Khayelitsha	2	Ngquba	10, 24	94 - 98	4 of the 8 sites have been invaded recently.
26 Nooiensfontein 2.000 Blue Downs 2 Welman 21 19 Professional relation 12 20 30 20 20. The Professional relation 12 20 20 20 20 20 20 20 20 20 20 20 20 20				•		0 : 1			The Instruction to Perform Work was issued to the Regional
The Social Housing Section is being engaged to gauge interest in development of these sites for beneficiaries who would qualify for social housing and GAP. The Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before a Clifton Pelican Park Phase 2 Retreat Pelican Park Phase 2 Retreat Soo Retreat A Carolus Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Strand St					_				Professional Team on 23 Jul 2020. The Professional team will
27 Ocean View Infill 28 Pelican Park Phase 2 1.900 Pelican Park 4 Abrahams 18 Fire Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. Clifton Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) Strand 2 Johan Brand 3 Strand 2 Johan Brand 3 Strand 2 Jaarsveld 3 Strand 4 Bernie Bernie In development of these sites for beneficiaries who would qualify for social housing and GAP. The Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the Department of Environmental Impact was finalised and Submitted to the The Vinch Park The V	26	Nooiensfontein	2.000	Blue Downs	2	Welman	21	19	
27 Ocean View Infill 397 Ocean View 19 61 for social housing and GAP. The Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department of Environmental Impact was finalised and submitted to the Department on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist nave been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the Stormy Planning applications have been submitted to the All three town planning applications have been submitted to the Stormy Planning Department and approvals with conditions have the Stormy Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been completed. Stormy Planning Department and approvals with conditions have been completed. Environmental study field work has been completed. Environmental study field work has been completed. Environmental study field work has been co									
Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) Strand Erf 5113 A.800 Strand Abrahams The Final Scoping Report (FSR) for the Environmental Impact was finalised and submitted to the Department of Environmental Affairs and Development Planning on 30 August 2020 which be followed by an Authority review period of 29 days before acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and awalt now input from Roads and Stormwater with regards to the main road that runs through the no go areas. All three town planning applications have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been obtained in undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be completed by the complete of the development framework report and plan must be completed.	27	Ocean View Infill	207	00000 \/:=	4	loos! D.::44-	40	0.4	
Pelican Park Phase 2 1.900 Pelican Park Abrahams 18 Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the no go areas. Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Strand 2 Johan Brand 3 Strand 2 Johan Brand 5 San-Marie Van Strand Erf 5113 4.800 Strand 2 Jaarsveld Bernie Bernie Was finalised and submitted to the Department of Environmental Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the no go areas. All three town planning applications have been submitted to the Town Planning applications have been obtained. Project Steering Committee members have been obtained. Project Steering Committee of the North following which the Undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the Erovinomental study field work has been completed. Existing services drawings complete. Geotech Phase 1 completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work following with contextual analysis. In terms of the Instruction to Perform Work following	21	Ocean view milli	397	Ocean view	4	Jose, Rutto	19	61	
Pelican Park Phase 2 1.900 Pelican Park 4 Abrahams 18 Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. Clifton Clifton Retreat 500 Retreat 4 Carolus Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand Strand 5 San-Marie Van Strand Erf 5113 4.800 Strand 2 Jaarsveld Bernie Affairs and Development Planning on 30 August 2020 which will be followed by an Authority review period of 29 days before acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the no go areas. All three town planning applications have been submitted to the Sp. 86, 86, 86, 85, 86, 100 planning Department and approvals with conditions have been obtained. Project Steering Committee members have been been obtained. Project Steering Committee members have been been completed. San-Marie Van 31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 8 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by development framework report and plan must be complete by an authority review period of 29 daxe before acceptance. The Water Use Licence Applications pecialist and Western Leopard Town Planning Development Tenework of the sites and Stormward design was done and await now input from Roads and Stormward design was done and await now input from Roads and Stormward design was done and await now input from Roads and Stormward design was done and await now input for Roads and Stormward design was done and									
Pelican Park Phase 2 1.900 Pelican Park Abrahams 18 67 acceptance is granted. Clifton Clifton Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Strand Strand 2 Johan Brand 3 Strand Stan-Marie Van Strand Erf 5113 4.800 Strand 2 Jaarsveld Bernie Mahier Abrahams 18 67 acceptance is granted. Clifton Clif									·
Pelican Park Phase 2 1.900 Pelican Park Abrahams 18 67 acceptance is granted. The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the 110 no go areas. Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 3 Strand 2 Johan Brand 3 Strand Park Phase 2 A quotation was received from the Regional Professional Team to undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by						Mahier			
The Water Use Licence Application Specialist and Western Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the Town Planning Department and approvals with conditions have been submitted to the Town Planning Department and approvals with conditions have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been contained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Project Steering Committee members have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members hav	28	Pelican Park Phase 2	1 900	Pelican Park	Δ		12	67	
Retreat 500 Retreat 4 Carolus 18 110 Leopard Toad Specialist have been appointed. A preliminary design was done and await now input from Roads and Stormwater with regards to the main road that runs through the no go areas. Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 8 100 Strand 8 100 Stran	20	I GHOUIT WINT HUGG Z	1.500	i Giloait i air	+ -	715141141113	10	07	
Retreat 500 Retreat 4 Carolus 18 110 design was done and await now input from Roads and Stormwater with regards to the main road that runs through the no go areas. Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 8 100 Strand 2 Johan Brand 8 100 Strand 2 Jaarsveld 8 100 Strand 2 Jaarsveld 8 100 Strand 2 Jaarsveld 8 100 Strand 100 Strand 2 Jaarsveld 8 100 Strand 100 St									
Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Strand Zuber and Strand Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Strand) Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Strand) Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Strand) Retreat Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Strand) Retreat All three town planning applications have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have									
Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for Change) Strand Strand Strand Strand All three town planning applications have been submitted to the Town Planning Department and approvals with conditions have been obtained. Project Steering Committee members have been obtained. Pr						Clifton			
Rusthof Infill Project (ex. Beverley Hills /Erf 5822 (Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 388 Strand 2 Johan Brand 389 Strand 389 Strand 380	29	Retreat	500	Retreat	4	Carolus	18	110	o o
(Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 8 100 San-Marie Van 31 Strand Erf 5113 4.800 Strand 2 Johan Brand 3 Strand 4.800 Strand 3 Strand 4.800 Strand 5 Johan Brand 8 Johan Brand 9 Johan Bran					1		1		
(Traffic Site development) /Erf 13051 (Mothers for 30 Change) 387 Strand 2 Johan Brand 8 100 seen obtained. Project Steering Committee members have beer selected. A quotation was received from the Regional Professional Team to undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the 100 team will commence. 388 Strand 387 Strand 2 Johan Brand 8 100 team obtained. Project Steering Committee members have beer selected. A quotation was received from the Regional Professional Team to undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been obtained. Project Steering Committee members have been completed. Environmental study field work has been completed. Environmental study fie		• ` `						05.00	Town Planning Department and approvals with conditions have
A quotation was received from the Regional Professional Team to undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the 31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 8 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by					_		_		been obtained. Project Steering Committee members have been
San-Marie Van 31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 4.800 Strand 2 Jaarsveld Bernie to undertake a Development Framework of the sites in order to determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by	30	Change)	387	Strand	2	Johan Brand	8	100	
31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 4.800 Strand 2 Jaarsveld Bernie determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by									·
Van determine the develop ability of the land. Currently in process of finalising the Instruction to Perform Work following which the 31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 8 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by						San-Marie			
31 Strand Erf 5113 4.800 Strand 2 Jaarsveld 8 100 team will commence. Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Environmental study field w									
Technical field work complete. Geotech Phase 1 completed. Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by	24	Strand Erf 5112	4 900	Strond	2		_	100	
Environmental study field work has been completed. Existing services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by	31	Olianu Eli Di io	4.800	Suanu	_	Jaaisvelü	8	100	
services drawings complete. Town planner busy with contextual analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by									
Bernie analysis. In terms of the Instruction to Perform Work issued the development framework report and plan must be complete by									
Bernie development framework report and plan must be complete by									
						Bernie			
	32	Strandfontein	1.400	Strandfontein	4	Wentzel	23	43	
	a		<u>.</u> 1			•	•	•	

33	Vlakteplaas	4.800	Strand	2	San-Marie Van Jaarsveld	8	The Town Planning application was advertised from 07 August 2020 to 7 September 2020. The Town Planner will now address all the comments received during this period and make the amendments to the layout plan where necessary
34	Vrygrond	665	Muizenberg	4	Mahier Abrahams	18	The Town Planning consultant has begun the process of engagement with the CoCT Planning Department to try and resolve the ownership status of the existing road reserves on the project site. A Project Steering Committee (PSC) must still be established.

No	Construction Tenders	Tender Type	Potential Units	Area	Region 1,2,3,4	Project Manager	Sub-Council	Ward	Comments on Progress - 10 September 2020
	Delft Symphony Way Corridor (ACSA)					Grobler			The construction tender for Bulks and internal services (sites) w be advertised during October 2020. Supply Management to
	(Site A)	Bulks, Civil	1.586	Delft	3	Basson	5	2, 108	confirm advertise date.
2	2 Greenville UISP	Civils	966	Fisantekraal	1	Shaun Moodley	7	105	Design and phase planning for remainder of the site is in progress. Phase (decanting) plan is dependant on existing Eskom infrastructure. Informal farmers to be relocated during September 2020.
(Harare 190 (Ilitha park 190)	Civils, T/S	190	Khayelitsha	2	Feziwe Ngquba	10	98	Engineering designs has been submitted, awaiting approval. Draft tender document has been submitted and 1st Bid Specification Committee meeting was held on 28 July 2020. Tender for the installation of services and construction of top structures is anticipated to be advertised during October 2020.
4	Maroela North	Bulks, Civil	1.687	Kraaifontein (Wallacedene / Bloekombos)	1	Shaun Moodley	2		Bid Specification Committee meeting No.1 complete. Project sit was invaded recently.
				,					Tender timeline has been agreed with Supply Chain Management (SCM). SCM to advise as to 1 st BSC meeting date
;	Pooke se Bos	Bulks,Civil,T/S	135	Gatesville	3	Neil Williams	11	46	
(Sir Lowry's Pass Village	Bulks,Civil,T/S	307	Sir Lowry's Pass	2	van Jaarsveld	24	84	Tender 67Q/2020/21 is currently being advertised (4 Septembe 2020 until 6 October 2020). A tender clarification meeting is scheduled to take place on 17 September 2020.

No.	Under Construction	Construction Type	Units	Area	Region 1,2,3,4	Project Manager	Sub-Council	Ward	Comments on Progress - 10 September 2020
1	Atlantis Kanonkop Phase 1	Top Structures	455	Atlantis	1	Rivaaj Mahabeer	1	32	The services of a contractor have been procured on a limited bid application through the Department of Human Settlements to complete the 13 outstanding units and repair 6 fire damaged units. Work will commence during October 2020.
2	Beacon Valley (Erven 44229, 45867, 3	Bulks, Civil	979	Mitchell's Plain	2	Grobler Basson	9	116	The City obtained a court order on 10 September 2020 to prevent vandalism and threats to the contractor on site. Construction commenced again.
3	Beacon Valley (Erven 42911 and 4291	2Bulks, Civil	831	Mitchell's Plain	2	Grobler Basson	9	116	The City obtained a court order on 10 September 2020 to prevent vandalism and threats to the contractor on site. Construction commenced again.
4	Belhar Pentech	Top Structures	340	Belhar	3	Ryan Thomas	6	12	Phase 1 - 11 units have been handed over in August 2020. The contractor has been advised by the Employer (Province) that their scope will be reduced from 207 to 101 units due to poor performance. The remaining units will be completed by the City's panel of contractors. Phase 2 - a total of 12 - 16 units will be completed by the end of September 2020.
5	Delft The Hague Phase 1 (VHP)	Top Structures	106	Delft	3	Shaun Moodley	5	13	Contractor is currently working on 11 new units and 15 vandalised units. Planned completion of all units is September 2021.
6	Delft The Hague Phase 1 (Power)	Top Structures	376	Delft	3	Shaun Moodley	5	13	The contractor has commenced with the first 60 units which will be completed towards the end of October 2020.
7	Dido Valley	Top Structures	600	Simon's Town	4	Clifton Carolus	19	61	The 1st contactor has started on the 6th August 2020 with the first foundations. The second contractor will follow once all his funding approvals are in place.
8	Greenville Phase 2	Top Structures	507	Fisantekraal	1	Shaun Moodley	7	105	Last 44 units in this phase achieved practical completion 0n 5 August 2020. Units were handed over to beneficiaries on 12 August 2020
9	Greenville Phase 2.1	Civils	562	Fisantekraal	1	Shaun Moodley	7	105	Practical completion of sites planned for end September 2020
10	Greenville Phase 3	Top Structures	562	Fisantekraal	1	Shaun Moodley	7	105	Contractor is progressing in line with programme, 24 units was completed at the end of August 2020

									There are two active contractors on site who have completed
									only 15 % of the works to date . As result of the delays the
									contractors will not be able to complete 100 units as planned by the end of November 2020. Only 50 units will be completed
11	Gugulethu Infill - Erf 8448	Top Structures	571	Gugulethu	4	Jose' Britto	14	38	according to their latest update programme.
	Cagalogia IIIIII Eliforio	10p Ottaotaics	071	Ougulotilu	-	JOGG BIRRO		00	One contract has been terminated and a new contractor will be
									appointment. The second contractor has resumed with
									construction on site. According to the latest programme, the first
12	Gugulethu Infill - Mau Mau (erf 2849)	Top Structures	434	Nyanga	4	Jose' Britto	14		units will be handed over during November 2020.
	,	,		, 0		Feziwe			The installation of electrification cable is in progress. All sites
13	Harare Infill	Bulks, Civil	900	Khayelitsha	2	Ngguba	10	02 08	anticipated to be complete by end of September 2020.
10	Tididio IIIIII	Duiks, Civii	300	Milayontona		Пучара	10		Bulk excavation at gabion wall site commenced mid-July after
									appointment of CLO on 15th July and local labour on 22nd July.
									Bulk excavation is 25% completed. The project practical
						Bernie			completion date will be extended by 32 days from the current
4.4	Imizamo Yethu - Phase 3	D II 0: II	000	Haut Day	,		46	7.4	practical completion date: 12 February 2021. due to lockdown
14	IIIIZamo femu - Phase 5	Bulks, Civils	922	Hout Bay	1	Wentzel	16		delay.
						Quintus			Contractor on programme. Phase 1 completion of 634 sites at the end of March 2021 and the contract May 2023.
15	Macassar	Bulks, Civil, T/S	2.469	Macassar	2	Welman	24	109	and that of Maron 2021 and the contract May 2020.
	Madadda	Buiks, Olvii, 170	2.400	Madadda	_	Womian		100	The last 273 units needs to be built on the last 2 project sites
									The Contractor has setup camp in the first week of August 2020.
						Clifton			The first kick-off meeting was held on the 6th August 2020.
16	Manenberg	Top Structures	555	Manenberg	4	Carolus	11,17	42,46	Additional security will be provided on both sites.
									Civils contract interrupted with only 1 month left to complete the
									project. Wallacedene Temporary Relocation Area members
									threatened and intimidated the contractor and site staff. They are
									disputing the approved beneficiary allocation split. The Contractor is therefore off site and contract has and contract has
									lapsed. The Project Steering Committee is busy engaging the
						Shaun			Temporary Relocation Area to find a way forward. Once resolved
17	Maroela (South)	Bulks, Civil, T/S	570	Kraaifontein	1	Moodley	2	111	a Deviation report will be submitted to BAC for contractor to
.,	Maroeia (Oddir)	Buiks, Civil, 1/3	370	Maanonten	'	Woodley			Complete project All 156 houses at Erf 5131 project site have been handed over to
									beneficiaries. At the Erf 1912 site, 42 houses are complete
						Bernie			except for electrical connections, with the last 33 houses in
18	Masiphumelele Phase 4 (PHP Project)	Top Structures	227	Kommetjie/Noordh	4	Wentzel	19	69	various stages of construction.
									Building plans for the toilets structures on the 70 serviced sites
									have been approved and construction of the toilet structures will
									commence during October 2020.
19	Morkel's Cottage	Bulks, Civil, T/S	547	Strand	2	Johan Brand	8	85,86	The survey of the illegal occupants is ready to commence and will be done by our Regional Professional Team.
	g-	24, 3, 7.7	0					00,00	We have been advised by Legal Services that the settlement
									negotiations have been accepted in principle by both parties. All
									that remains is to get approval from Mayco to settle the matter on
									the agreed terms. Legal is working towards the next Mayco
						Ryan			meeting which is scheduled for 15 September 2020. If approved,
20	Morningstar Durbanville	Bulks, Civil, T/S	166	Durbanville	1	Thomas	7	112	the settlement will be made an order of court and will then conclude the matter
	-		148 top						Turnkey developer returned to the site on 4 May 2020 and
			structures						commenced with the construction of the top structures on 11
			and 2						May 2020. First 32 houses were completed by the end of
			serviced						October 2020.
21	Somerset West	T/S	sites = 150	Somerset West	2	Johan Brand	24	15	
-' -	Comprode Front	.,5	5.100 - 100	Comordot Wood	-	Cecelia	۲-		It is envisaged that work on site (bulks) will start in October 2019.
						Thiem/Provin			Substitution of the following will older in October 2010.
22	Shoffield Bood (City 9 Drawings)	Duller C' "	200	Dhilinni	,	•	10	25	
	Sheffield Road (City & Province)	Bulks, Civil	388	Philippi	4	cial Project	13	35	First top atrusture contractor on site and completed the first 90
22									First top structure contractor on site and completed the first 30
22			Į.						foundations for units which will be completed mid December
22									foundations for units which will be completed mid December 2020. Two additional contractors will start during October 2020
	Valhalla Park			Valhalla Park		Noluvuyo Bidli			foundations for units which will be completed mid December 2020. Two additional contractors will start during October 2020 with 30 units each. The contractor for the completion of the

1.2 Housing Development - Social Housing Projects - 10 September 2020

Social Housing	_		POTENTIAL YIELD		
Projects in Planning Stage	Area	Comments on progress - September 2020	Social/ Transitional Housing	GAP	
Pine Road	Woodstock	 Due to delays of Covid 19, building plans to be submitted at the end of October 2020 Geotech approved in principle June 2020 pending bugdet availability in Juanuary 2021 adjustment budget. Building approval submission targeted for end October 2020 Contractor procurement by end October 2020 for construction start beginning January 2021 	230		
Dillon Lane	Woodstock	Public participation is currently in process.	230		
Fruit & Veg Site	Zonnebloem	The site will be advertised once reservation is approved. Department is consulting with subcouncil about concens of reservation. SHI will be allocated once reservation is approved.	50		
Pickwick	Salt River	Stedone consultants appointed to Rezone the site. The Department is working with Stedone consultants in the rezoning process. Progress is currently unfolding	600		
Erf 14888 New Market Street	Salt River	Request for quotation (FRQ) issued to GladAfrica to rezone the site. Cosing date for RFQ is 15 September 2020 GladAfrica should start the rezoning process in October 2020.	300		
Salt River Market	Salt River	Department is currently meeting with Communicare to confirm if they will be able to implement the project OR we should appointment of one of the City's Social Housing Partners to take over the implementation of the Social Housing part of the project. These negotiations will be completed by end of November 2020. Department has drafted a request final Approval by Council to release the site to for Social Housing Development by February 2021. Next step is to redesign the development scheme and building plans submission by end of June 2021.	800		
Woodstock Hospital Site	Woodstock	Final feasibility assessment report submitted by June 2020. Instruction to Perform Work (IPW) issued to Stedone to Rezone the site for affordable housing on the 09 September 2020. Rezoning process to start in 01 October 2020 The property has been transferred to the City's name 0n 09 September 2020	500		
POS next to Woodstock Hospital	Woodstock	Request for Qotation (RFQ) for the site sill to be issued after the illegal occupiers have been evicted. Property management department is dealing with the eviction process.	200		
Erf 12010 & 12011 James Street	Salt River	RFQ for the rezoning of the site will be issed once the budget is approved in the January 2021 adjustment budget.	50		
Parow Precincts: Parow Erf 14272 / 22550 and others. See Parow Package.	Parow Precincts	RFQ for the rezoning of the site was issued in September 2020. Department is in the process to appoint SHI to implement project.	2249		
Erf 62594	Lansdowne	· To commence land release process to Agri Housing	460		
Mountain view	Brackenfell (Madulammoho)	Project in abayance due to rejection by the subcouncil and community.	200		
Erf 23889, Maitland	Maitland	Land release finalised and building plans to be submitted in October 2020. Finalising confirmation of funding Sources	200		

SOCIAL HOUSING	Area	Comments on progress - September 2020	POTENTIAL YIELD			
PROJECTS UNDER CONSTRUCTION	Alea	Comments on progress - September 2020	Social/ Transitional Housing	GAP		
Bellville	Glenhaven (DevMark)	Phase one of the project is now complete. Phase two is underconstruction.	512	253		
Conradie Hospital Site	Pinelands & Thornton	 Construction of bulk infrastructure complete. Planning processes completed. Construction on Phase 1 (620 units) projected has started. 	1236			
Goodwood	Goodwood Station (DCI)	Relocation of overhead powerlines is currently underway.Finalising procurement of top structure contractor	1080			
Heideveld	Heideveld Station (DCI)	 Discussion with SHRA and Province re cancellation of Social Housing due to volatile local conditions 	183			
Mitchells Plain	Weltevreden Valley (Povicom)	 Phase one is completed. Site visit has been planned for September with Mayco member. 	104			
Bothasig Phase 2	Bothasig (Communicare)	 Construction very advanced. Site visit has been planned for September with Mayco member. 	314			

ANNEXURE 2.1 INFORMAL SETTLEMENTS PROJECTS MONITORING REPORT

1. INTRODUCTION

The City of Cape Town's Five-Year Integrated Development Plan (IDP) represents the over-arching strategic framework through which the City aims to realise its vision for Cape Town.

This is done by building on the five pillars of a Caring City, an Opportunity City, an Inclusive City, a Safe City, and a Well-run City.

The informal Settlements Department's objectives aligning with the five pillars are described in the IDP document and aligned as indicators and targets forming part of the Departmental SDBIP and the Department's performance and progress can be measured against these targets.

This report aims to highlight progress on projects within our Informal Settlement Portfolio to deliver on planned financial and non-financial targets for the current financial year.

The specific indicators used to measure delivery on non-financial targets are described as follows:

Corporate Objective 3.2.: Mainstreaming Basic Service Delivery to Informal Settlements and Backyard Dweller

- 3.N Number of sites serviced in the informal settlements
- 3.L Number of service points (toilet and tap with hand basin) provided to backyarders residing on city owned land (housing rental property

SFA 3: THE CARING CITY

Corporate Objective 3.2.: Mainstreaming Basic Service Delivery to Informal Settlements and Backyard Dweller

3.N Number of sites serviced in the informal settlements

This indicator measures the number of serviced sites delivered in Informal Settlements.

Projects reflected in this report are current and will continue to yield sites in the ensuing financial years.

As at the end of June 2020 the department delivered 924 serviced sites which exceeded the planned target of 850 sites for the 19/20 financial year, it is important to note that the delivery of these service sites was achieved under challenging circumstances.

The non-financial target for the current financial year is set at 1350 serviced site, and the contributing projects are listed as follows:

a) Imizamo Yethu Emergency Project, Hout Bay


The Imizamo Yethu Emergency Project was initiated after a devastating fire took place in March 2017, which left approximately 2 500 households razed. To assist the conditions warranting an emergency dispensation, the Informal Settlements department met with the affected residents to rapidly resolve the emergency situation. It was agreed upon that the City will construct temporary emergency units to house the displaced residents, whilst executing a "Super-Blocking" upgrading. This upgrading includes improving and creating access tracks/roads; upgrading the electricity network and improve the lighting; upgrading the water and sewer networks as well as installing ablution facilities.

Project Progress:

- Three Temporary Relocation Ares (TRA), namely Depo Site, Disa Site and Triangle Site TRA, have been completed two of which are occupied by fire victims.
- Due to resistance experienced from the community related to the original implementation plan and subsequent legal proceedings, in March of 2019
 The Project team activated an alternative development plan to improve access and basic services to the area:
 - The alternative plan includes the construction of roads 4,2 and 5, related walkways and the re construction of an existing derelict road currently being used as the primary access route around IY
 - Road 4 & 2 progress are as follows:
 - 75% of construction related to the sewer networks, water networks and roadways are nearing completion.
 - Road 5, 90% complete including a primary walkway from road 5 to Peterson including all related infrastructure.

Due to lengthy court proceedings and multiple project stoppages our contract period expired and we have submitted a BAC report for extension of contract sum and period has been submitted for signatures and is anticipated to serve at BAC within the next 2 – 3 weeks.



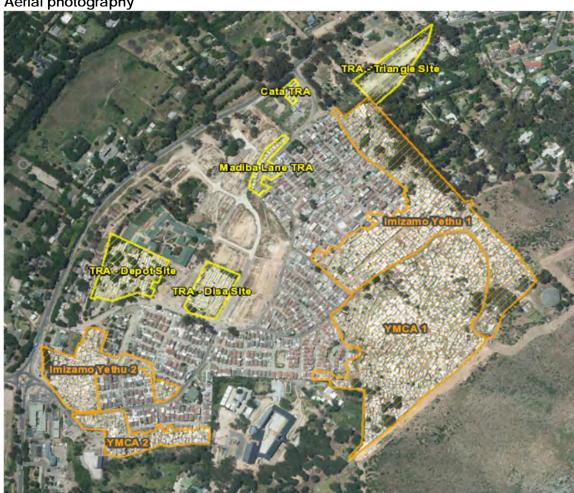

Construction progress pics



b) Deep Freeze, Macassar

The Deep Freeze Informal Settlement is situated on Erf 5351, Macassar located within the south-eastern part of the metro between the suburb of Khayelitsha to the west and Somerset West to the south-east. The site extent is 11.77 hectares and is occupied by 171 households, of which 35 are brick and mortar and the remaining 103 informal structures. The settlement has limited basic services available to informal households. This project will create 440 individual services site to qualifying beneficiaries.

Project Progress:

- 60% of the planned bulk infrastructure (water networks, sewer networks and roadways) are complete.
- Due to unforeseen additional works a MFMA section 116 report was required
 to extent the original contract period and value to absorb additional time
 required to complete the project, this process is currently underway for the
 extension of contract period beyond the 3-year budget cycle.

Aerial Photography



c) Backstage 1, Khayelitsha

The Backstage 1 project will be established on Erf 36638, in the suburb of Khayelitsha. The settlement is bounded by Ncedo and Galela Street and will benefit 250 households from various locations surrounding the site. The existing households on the proposed site are living in highly densified configurations and the settlement has limited basic services available to informal households. The approved project layout makes provision for 250 erven at approximately 75m² and a public open space.

Project Progress:

- The civil engineering infrastructure, which is currently underway, will include service sites, roads, sidewalks, and water and sewer networks.
- Project commenced in March 2020 and is anticipated to be completed in January 2021.
- This project is under continues threat of land invasions which could impact the project programme, cost and time.

Settlement Aerial photography



Construction Progress pic



d) Garden Cities, Mfuleni

The Garden City Informal Settlement is situated in southern periphery of Mfuleni within the City of Cape Town. The settlement is on Erf 28 and a portion of Erf 327 and is approximately 6.24ha in extent.

There are limited basic services available to the residents of the informal settlement. This development will create 467 housing opportunities in terms of individual service sites to qualifying beneficiaries in the informal settlement and surrounding, as well as formalized civil engineering infrastructure (water reticulation and sanitation networks, as well as a stormwater management), paved access roads and pathways.

Project Progress:

- The project commenced in November 2019 and is anticipated to be completed in March 2021.
- A surge in illegal land invasions poses a threat to project programme, cost and time. Matter being monitored and engagement with relevant stakeholders underway.
- Contractor is on site and progressing as planned.

Aerial Photography



Construction Progress pic



e) Wallacedene 4 in 1, Kraaifontein

The Wallacedene 4 in 1 Informal Settlement is situated on Erf 12996 in Kraaifontein. The settlement is resident to approximately 150 households which is are exposed to poor living conditions, with structures found in highly densified configurations. The densification prevents residents' accessibility to minimal municipal and emergency services. The following services will be implemented: 269 service sites, water reticulation, sewer reticulation, road network, stormwater runoff, electricity reticulation, individual standpipes and toilet structures.

Project Progress:

- Project commenced in January 2020 and is anticipated to be complete by March 2021.
- The contractor is currently on site to complete the civil engineering services.
- Illegal land invasions pose a threat to project programme, cost and time. Matter being monitored and engagement with relevant stakeholders underway.

Aerial photography



Progress Pics





f) Better Life, Mfuleni

The Better Life greenfield site is situated in Mfuleni. This development will create 117 housing opportunities in terms of individual service sites to qualifying beneficiaries in the surrounding area, as well as formalized civil engineering infrastructure (water reticulation, sanitation networks, and stormwater management), paved access roads and pathways.

Project Progress:

- The project commenced in March 2020 for a duration of 12 months.
- The contractor is on site and the implementation of the formalised civil engineering infrastructure is progressing as programmed.
- A surge in illegal land invasions poses a threat to project programme, cost and time. Matter being monitored and engagement with relevant stakeholders underway.

Construction progress pics





g) Freedom Park, Ottery

The Freedom Park Informal Settlement is situated in Ottery. The settlement was established nearly 40 years ago, as residents were relocated from various farms and roadways in the surrounding area and has grown exponentially over the years. The project approved layout makes provision for 159 individual service sites, bulk water and sewer networks as well as roadways.

Construction is planned to commence in the latter part of the current FY, we anticipate a BAC approval to award a contractor within the month of September 2020.

Aerial photography



h) Monwabisi Park, Khayelitsha

The Monwabisi Park Informal Settlement is located in Khayelitsha bordering False Bay coastline. The settlement measure approximately 90 hectares, a portion of the site along the southern boundary is covered in Cape Flats Dune Sandveld and is within the Wolfgat Conservation Area Biodiversity Network (CBA 1B), ±2000m² will be removed for the purpose of the development. The landscape has not changes from its natural state, apart from vegetation that has been removed in order to erect structures.


The original settlement has limited basic services available to approximately 24 000 residents and 6 472 household dwellings The settlement has experienced a surge in land invasions since 2018, these occupants do not form part of the planned project.

The vision of the upgrade is to incrementally upgrade the settlement by building a safe and integrated community without relocating people outside of the area.

The following services to be provided: Sewer and Water Reticulation network; Construction of Roads and Storm Water Management System; Electrification; Individual serviced sites to qualifying beneficiaries.

The first phase of the project is currently in a SCM process The tender document for the civil engineering services has been advertised and currently in the evaluation stage of the of the procurement process.

Aerial photography

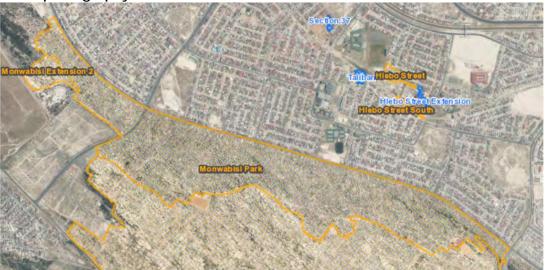

Proposed 1st phase layout



i) Backstage 2, Khayelitsha

The property (hereinafter referred to as Erven 59046, 59047 & 59048) is located in Khayelitsha in the suburb of Kuyasa just off Ntlazane Road within Ward 97. The site measures 4.52ha in extent and aim at delivering 466 residential opportunities and ancillary uses.

The tender document for the civil engineering services has been advertised and currently in the evaluation stage of the procurement process.

Areal photography

As a result of recent land invasions this site has been invaded 100%

Aerial photography



Proposed layout



j) Barney Molakwana Section, Khayelitsha

Barney Molokwana Section Informal Settlement, also known as BM Section, is situated in Khayelitsha suburb on Erf CA544-0-3. The settlement is densely populated by informal structures, part of which is encroaching on the wetlands located in the centre of the settlement. There are approximately 4230 informal structures, approximately 1700 of which are located in risk areas (under power lines and in low-lying / flood prone areas), whilst the remaining 2530 are located in areas considered to be developable.

The City of Cape Town embarked on a process of establishing the appropriate land use rights in order to incrementally upgrade the settlement over multiple phases, the 1st increment will include primary road and civil engineering infrastructure.

The project is currently in its final planning stages and subsequent detail engineering design.





k) Enkanini, Khayelitsha

The Enkanini Informal Settlement, situated in the southern boundary of Khayelitsha, is one of the largest informal settlements within the City of Cape Town. Due to the high density of the settlement, there are limited basic services available to the informal households. Phase 1 of Enkanini – Zwelitsha, was completed in 2009, however, approximately 11 000 households still reside in the larger informal settlement. The informal settlement is approximately 125 ha in size and is prone to seasonal flooding and fires.

Ongoing land invasions has impacted our project progress

The project is currently in a detail engineering design phase, with commencement on site intended in the 21/22 FY.

The settlement will be upgraded incrementally over the next 8 years,

Aerial Photography



Proposed layout plan



I) Enkanini South TRA, Khayelitsha

Rapid growth of informal settlements and illegal occupation of land remains one of the core developmental challenges facing the City of Cape Town. In addition, these informal settlements, specifically those that have no services, are considered high risk areas, in relation to health issues, which have been highlighted with the current Covid-19 pandemic. Accordingly, the directives issued in terms of the Disaster Management Act, 2002, in response to the Covid-19 pandemic, have instructed Metropolitan Municipalities to take measures with specific reference to Human Settlements: areas of overcrowding specifically within informal settlements and steps to allow for dedensification.

The Informal Settlements department has identified the remainder Erf 18332 Khayelitsha, to develop the Enkanini Temporary Relocation Are (TRA) to densify various informal settlements in the surrounding area, especially benefitting the greater Enkanini UISP project. The specific Temporary Relocation Are (TRA) is located close to the intersection of Mew Way and Baden Powell Drive.

It is anticipated that potentially between 3500 to 4000 residential units with the associated school, community, religious and business sites can be accommodated in the Enkanini South development.

Statutory planning studies, processes and approvals are currently being carried out by the Informal Settlements Planning department.






m) Driftsands, Mfuleni

The Driftsands project is made-up of three (3) Informal Settlements located on the Driftsands Nature Reserve. Settlements to be included in the project is Green Park, Los Angeles, and Sophakama Informal Settlement, lying north of the N2 and east of the R300 highways.

The project is currently in the pre-planning phase and the initial intention was developing this settlement in conjunction with the Housing Development department to deliver various typologies: serviced sites; double storey row units; double and single story semi-detached units; double and single storey free standing units. Other designated land uses could include: community facilities, public open spaces, commercial / retail / service industry

As a result of recent mass land invasions a revised development plan is required as all the intended land associated to this project is illegally occupied.

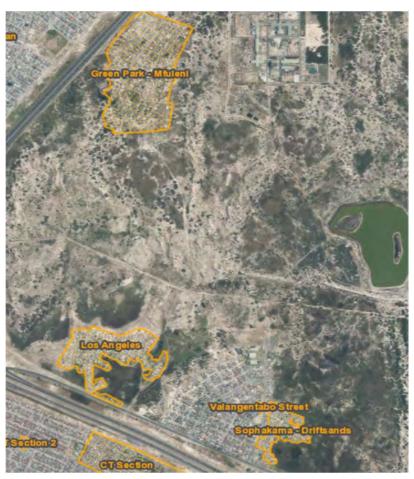

3.L Number of service points (toilet and tap with hand basin) provided to backyarders

The Backyarder Programme is implemented by the Human Settlements: Informal Settlements Department.

The services make provision for the installation of a precast concrete toilet structure, a toilet, a wash basin with a water dispensing device unit to backyard dwellers residing on City Rental Stock properties.

Once service points are complete, the Electricity Generation and Distribution unit carry out the design and implementation of electricity connections based on the existing infrastructure capacity.

As of the end June 2020 the department has deliver 428 backyarder service points, exceeding the annual target of 300 service points.

The delivery target for the current financial year as per the Corporate Scorecard is 350 service points.

Areas of implementation for 2020/21:

- 1. Parkwood
- 2. Hanover Park
- 3. Bellville South
- 4. Mitchells plain
- 5. Lavender hill

Project Challenges/Risks:

- All backyarder projects are at risk daily due to gang violence and intimidation.
 Safety of staff and contractors must take first priority when working in these high risk areas.
- Access to the backyarders has been denied by the tenants inside the rental units due to delays experienced with the maintenance of the rental units.
- Services refusal by Backyarders.

Access to existing infrastructure, causing lengthy installation processes.





Photos: Site inspections in Lavender Hill, Parkwood and Bellville South

Number of top structures erected in the informal settlements (EHP)

The indicator will measure the number of Top Structure units erected in Informal Settlements. The construction of Top Structures units is not the core function of the Human Settlements: Informal Settlements department. Top structures are only provided on Emergency Housing Programme (EHP) projects, and this is difficult to quantify, as emergencies cannot be predicted.

Indicator definition: The Programme is instituted in terms of section 3(4)(g) of the Housing Act 1997 and will be referred to as the National Housing Programme for Housing Assistance in Emergency Housing Circumstances. Essentially, the objective is to provide temporary relief to people in urban and rural areas who finds themselves in an emergency state as defined and described in the National Housing Code.

As of the end June 2020 the department has deliver 807 Top Structure units (Bosasa IDA: 687; Sir Lowry's Pass Village 120), against the target of 500. The target as per the Informal Settlements SDBIP for the 2020/21 financial year is 229.

National Treasury has decreased the HSDG funding for the City of Cape Town, which is specifically used for the construction of EHP Top Structure units. This will have a direct impact on the delivery of non-financial targets.

Areas of implementation for 2020/21:

1. Bosasa IDA

Aerial Photography



Progress pics



Ravensmead IDA:

Aerial Photograph



Construction progress pic



Conclusion

The projects highlighted in this report has a direct impact on the current financial year budget, all projects in a prefeasibility and planning phase is designed and managed in house and listed against this report as annexure A.

2.2 Human Settlements - Informal Settlement Upgrades: Current Project Portfolio Project Phase: Construction and Detailed Design

			,					
No.	1. Under Construction	Upgrading Type	No. of beneficiaries	No. of Sites Completed	Area	Area 1,2,3,4	Comments on progress - September 2020	Planned Start Date & Planned Completion Date
1	Imizamo Yethu IS Emergency Project Project Manager : Siraaj Samsodien	Superblocking	N/A	N/A	Hout Bay	1	Project progressing as programmed. BAC report for extension of contract period and sum has been submitted for signature to absorb delays related to court procedings and community reistance.	Start Date: September 201 End Date: June 2020
2	Deep Freeze: Services Formal Area Project Manager : Siraaj Samsodien	Serviced Sites/	440		Macassar	2	Contractor is appointed, Contract deviation underway to absorb multiple delays and additional contractual cost related to existing undergrown inrastructure not shown on wayleaves.	Start Date: March 2019 End Date: June 2020
4	Backstage 1 Project Manager : Luxolo Madubedube	Partial greenfield : service sites	250		Khayelitsha	2	contracor is on site and Project progressing as planned. Illegal land invasions poses a threat to project programme, cost and time. Matter being monitored and enagagement with relevant stakeholders underway.	Start Date: March 2020 End Date: October 2020
5	Garden City Project Manager : Randell Marinus	UISP- Serivce sites	467		Mfuleni	2	contractor is on site and Project progressing as planned. Illegal land invasions poses a threat to project programme, cost and time. Matter being monitored and enagagement with relevant stakeholders underway.	Start Date: November 201 End Date: November 2020
6	Wallacedene (4 in 1 plus) Project Manager : Diaan Rangole	Partial greenfield : service sites	269		Kraaifontei n	3	contractor is on site and progressing as planned. Issues realting to development forum and illegal land invasions poses a threat to project programme, cost and time. Matter being monitored and enagagement with relevant stakeholders underway.	Start Date: January 2020 End Date: December 2020
7	Better Life Project Manager : Densil Faure	Green fields, service sites	117		Mfuleni	2	Contractor is on site and progressing as planned. Issues related to development forums and lilegal land invasions poses a threat to project	Start Date: January 2020 End Date: July 2020
	Backyarder Programme (This programme provides a precast concrete toilet structure, tap stand and wash basin to backyard dwellers on City rental upits.) Installation and	Backyarder W&S Services Backyard					Contractor progressing as programmed. Ongoing general matters impeding the Backyarder Program progress: a). Services refusal by Backyarders. b). Access to existing infrastructure, causing lengthy installation processes.	
9	maintenance of Water Dispensing Device with supporting management software for Informal Settlements and Backyarders on City Rental stock. Project Manager: Randell Marinus	Water Dispensing & Management (This programme provides WDM to backyard dwellers on City rental units.)		406	City W	ide	contractor to stop work and return on days when it is safe to do so. Areas of implementataion: 1. Parkwood 2. Bellville South 3. Hanover Park 4. Mitchells Plain 5. Lavender Hill/Steenberg	annual Programs
10	Emergency Housing Programme EHP: Project Manager : Siraaj Samsodien	Emergency Top Structures	Various	200	City wide	City wide	Bosasa IDA: - Project progressing as programmed 617 units has been completed as at the end of Q3 2019/20 Contractor's currently on site to complete remaining units and plumbing installations. Anticipated completion 30 September 2020. Ravendmead: - Phase 1 deisgn and civil construction complete: - Phase 1 EHP Top Structure contractor on site and progressing as planned. Sweet Homes Farm (balance of EHP top structures): our contractor requires law enforcement to acomapny them to start building, due to capacity issues law enforcement is unable to assist (very voitle area, and contractors are	annual Programs
11	Hida Park (Hangberg) Project Manager : Siraaj Samsodien	UISP- Rudimental services	N/A		Hout Bay	1	contractor on site and has initiated works related to engineering serivces	Start Date: June 2020 End Date: 30 June 2021
No.	Engineering Design Stage Compiling Construction Tender Documents	Upgrading Type	No. of beneficiaries	No. of Sites/Units Completed	Area	Area 1,2,3,4	Comments on progress - September 2020	Anticipated "Start Date" & "Completion Date"

1	Monwabisi Park Project Manager : Nondyebo Msolo	UISP Super Blocking	7000		Khayelitsha	2	project currently in a SCM evaluation stage, 1st BEC scheduled for 01/10/2020	Feb 2021-june 2023
2	Backstage 2 Project Manager : Luxolo Madubedube	UISP			Khayelitsha	2	project is currently in an SCM evaluation stage however 100% of the project land has been invaded	July 2021-June 2022
3	Enkanini Project Manager : Diaan Rangole	UISP	7.500		Khayelitsha	2	Consultants progressing as planned with engineering designs, Tender document to be ready by November 2020	Start Date: September 2019 End Date: May 2027
4	Enkanini South TRA Project Manager: Gerard Hanekom and Diaan Rangolie	TRA	3.500		Khayelitsha	2	detailed engineering desing currently underway, a constrcution term tender to be used for the construction of civil engineering serivces, contractor to be appointed by November 2020	October 2020-June 2022
5	Sweet Homes IDA & UISP Phase 2 Project Manager : Nondyebo Msolo	UISP Super Blocking	3,040	TBD	Philippi	4	Project currnelty being packaged for implementaion by a term contractor to carry our constrcution of engineering services.	Phase 2: Start Date: January 2021 End Date: TBD
6	Barney Molokwana Section Project Manager : Luxolo Madubedube	UISP Super Blocking	4213		Khayelitsha	2	Await planning approval, and we are currently in the process of appointign a consultant to effect detailed engineeing design. Workshops will be set up with community to discuss revisions to layout and project scope.	TBD

2.3 Human Settlements - Informal Settlement Upgrades: Project Portfolio: Planning and Pipeline

			i idilililig c	and Pipeline		
No.	Planning and Pipeline Projects	Upgrading Type	No. of beneficiaries	Area	Area 1,2,3,4	Comments on progress -Sept 2020
	S-Section Planner : Sandiso Mgcimeni	UISP	4369	Khayelitsha	2	Pre Feasibility & Conceptual, proposed to be part of larger Provincial project- Need additional land
2	Tsepe- Tsepe Planner : Susan Groenewald	UISP	300	Khayelitsha	2	Land use planning to commence. De-densification site needed
	Backstage 3 Planner : Gerhard Hanekom	UISP		Khayelitsha	2	land invaded in July 2020
	Marikana Planner : Sandiso Mgcimeni	UISP	8000	Philippi	4	Pre Feasibility & Conceptual. Legal matter to be resolved. De-densification site needed for Superblock or UISP
	Kampies Planner : Sandiso Mgcimeni	UISP	250	Philippi	4	land use planning underway, land reservasion outstanding from property services
6	Mfuleni Ext 1 Planner : Gerhard Hanekom	UISP	500	Blue Downs / Mfuleni	2	Land use planning to commence. As part of the larger Mfuleni intergration delvelopment. Combined EIA to be commenced. Reservation approved
	Kalbaskraal Planner : Susan Groenewald	UISP		Lotus River		Outstanding Land Reservation
8	Phola Park <i>Planner: Susan</i> <i>Groenewald</i>	UISP Service sites	721	Gugulethu	3	Planning Application approved - required additiona land. De-densification site needed
	Enkanini - Revised Planner : Gerhard Hanekom	UISP	8151	Khayelitsha	2	Planning Application submitted - and approval recived for 7 phases
	Doornbach <i>Planner: Gerhard</i> <i>Hanekom</i>	UISP	3555		1	Planning Application canceled - Ready to submit revise application after appointment of consulting team for specialist study reports. Required additional land. De-densification site needed
	Lotus Park Project Manager : VPUU		1609	Gugulethu	3	Planning process underway, after land is transferred to the City. Prasa owned property. De-densification site needed
12	Village Heights Planner : Sandiso Mgcimeni	UISP	3188	Retreat / Seawinds	4	Land use planning application submitted. Consultants appointed for technicnal studies and prelim desgin Roll over site needed to be approved
	Klipheuwel Planner: Susan Groenewald	UISP	807	Klipheuwel	1	Road layout for electrification project is completed.
	Military Heights Planner : Sandiso Mgcimeni	UISP	107	Retreat / Seawinds	4	Reservation approved, require rolle over site - reservation for rolle over site submmitted.
	Enkanini - South Planner : Gerhard Hanekom	UISP		Khayelitsha	2	Land use approval in place for TRA, consultants appointed to commence with greater area planning and related technincal requirments.
	Bosasa Extension Planner : Gerhard Hanekom	UISP		Mfuleni	2	Subdivision plan to be submitted
	Racing Park TRA Planner : Gerhard Hanekom	TRA		Dunoon	1	project moved to province HS
	Bosasa Link Planner : Gerhard Hanekom	UISP		Mfuleni	2	Land use planning submitted. As part of the larger Mfuleni intergration delvelopment. Combined EIA to be commenced. Reservation approved
	Park Road Planner : Susan Groenewald	UISP		Phillipi	3	Land use planning submitted. As part of the Greater Erf 5268 delvelopment of catalitic project unit. Pre-feasebility planning
20	YAB section Planner : Sandiso Mgcimeni	UISP		Khayelitsha	2	Required additional land for project to commence
	Victoria Mxenge informal settlements Planner : Sandiso Mgcimeni	UISP		Khayelitsha	2	Reservation for sites other than S- section is submitted. Waiting outcome
23	Sondela Informal Settlement Planner : Sandiso Mgcimeni	UISP		Mfuleni	2	community requested reblocking and MOA to be signed with City.
24	Monwabisi Park M section Planner : Sandiso Mgcimeni	UISP		Khayelitsha	2	land use application submitted await approval.
25	Greater Monwabisi Park remainder Planner: Sandiso Mgcimeni	UISP		Khayelitsha	2	Planning consultants to be appointed.

ANNEXURE 3

PO Released to Vendor PO created (not released yet) Requisition No movement on WBS

2



BASELINE FY20/21 CAPEX PROJECT PLAN DATE: 25 JUNE 2020 BASELINE APPROVAL REV: 014 (18 SEPTEMBER 2020) LEGEND
Central Region
South Region
North Region
East Region

										84%	3%	2% CUREMENT STATE	5% 'US	5%
Department	WBS Element	WBS Element Description	Proposed(Approved) Budget 2020/21	Final Budget Cut 27.08.2020	Detail scope	Contractor	Name of Responsible Person	Name of Project Manager	Comment	Status	Requisition Number	4400 Number	PO Number	Date PO Issued to Vendor
Public Housing	CPX.0011374-F2	Plant & Equipment: Additional FY21	50 000.00		Plant & equipment purchse over a 12 month period as and when required	RFQ	Portia September	Sonia Fillies	Rresposible person and PM confirmed on PPM	PO released to vendor			4503734296	13 Aug 2020
Public Housing	CPX.0018261-F1	Major Upgrades - Old Flats Langa Ward 52	330 000.00		Upgrade to infrastructure at the Old Flats hostel Langa in ward 52 - fencing and boundary walls	TCC 243Q/2016/17 or NDG (50Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Rresposible person and PM confirmed on PPM	No movement on WBS				
Public Housing	CPX.0018226-F1	Upgrade Council Rental Units - Ward 65	120 000.00		Terence planning area lightning - TBC	Terence to Provide	Terence Bent	Zaahir Jassiem		No movement on WBS				
Public Housing	CPX.0018583-F1	Upgrade Flats - Ward 9 Bellville South	640 000.00		Upgrade Flats in Ward 9. New fascias, gutters and downpipes for Bellville South	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids		PO released to vendor			4503728630	06 Aug 2020
Public Housing-Top Level/Programme	CPX.0017086-F1	Area East Electrical Services	3 416 000.00		212Q, 128Q & 308Q (ELECTRICAL WORKS TERM TENDERS) are available to spend additional R3 000 000.00 increase. Obtain increase from CPX.0015782-F1 as 357Q/2018/19 (staircase term tender) to be cancelled due to local office as elegibility criterion deemd bias by AGSA.		Tivani Hlongwane	Zaahir Jassiem						
		Sub Level Project Total	282 053.94		eregionity circums decind bias by ACOA.									
Public Housing	CPX.0017086-F1.EM	Electrical services Macassar Blocks	282 053.94	282 053.94	Upgrade rental units in Area 4 by rewiring entire buildings -Macassar Blocks	212Q/2016/17 or 286Q/2018/19	Tivani Hlongwane	Zaahir Jassiem	Project packaging in progress Delta BEC					
Sub level / Project		ID No.10.24 Window Replacement in Elsies River, Clarkes Estate, Phase 3	-		Window replacement in Clarkes Estate (Glengarry Court)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids						
Sub level / Project		ID No.10.23.2 Windows Replacement in Elsies River, Clarkes Estate PH2.2	-		Window replacement in Clarkes Estate, phase 2.2 (Martindale, Hibberdene, Holmdene & Glencor courts)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids						
Public Housing-Top Level/Programme	CPX.0017148-F1	Major Upgr Area Central - Elec FY21	20 777 577.00		212Q, 128Q & 308Q (ELECTRICAL WORKS TERM TENDERS) are available to spend budget. Obtain increase from CPX.0015782-F1 as 357Q/2018/19 (staircase term tender) to be cancelled due to local office as elegibility criterion deemd bias by AGSA.		lan. Andre Davids	lan. Andre Davids	Await Goolam to finalise budget reduction post virement. Do not touch this budget.					
Sub-level / Project	CPX.0017148-F1.UM	CRU Electrical Upgrades	1 154 155.00	1 003 370.70	Electrical Upgrade to flats in Clarke Estate, Adriaanse, Leonsdale, Avenwood, Trinity- Place, Avon Estate. Complete installation of inclusive of new wiring, new distribution- board, new plug points, new batten holders, new switches	212Q/2016/17 or 286Q/2018/19	lan. Andre Davids	lan. Andre Davids	Project packaging in progress Delta BEC	PO created (not- released yet)			4503700024	21 Aug 2020
Sub level / Project	CPX.0017148-F1.WR	Window Replacement Elsies River	-		Window Replacement Elsies River		lan. Andre Davids	lan. Andre Davids	Sub-level Senior to window projects below.					
Sub level / Project	CPX.0017148-F1.WR.AW	ID No.10.20.2 Windows Replacement in Elsies River , Avonwood Phase 2.2	925 638.41		Window replacement in Avonwood, Phase 2 (Abottsdale and Airlie Place Court)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor			4503735138	25 Aug 2020
Sub level / Project		ID No.10.23.1 Windows Replacement in Elsies River, Clarkes Estate PH2.1	-		Window replacement in Clarkes Estate, phase 2.1 (Frere, Blanco, Luka, Marydale courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids						
Sub level / Project	CPX.0017148-F1.WR.L2	ID No.10.21 Windows Replacement in Elsies River, Leonsdale 2	1 000 144.10		Window replacement in Leonsdale 1(De Doorns, De Hoek, Zeerust, Steyning, Groenkloof, Bereaville, Devondale and Alicedale Courts)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor			4503735139	25 Aug 2020
Sub level / Project		ID No.10.22.2 Windows Replacement in Elsies River, Clarkes Estate Phase 1.2	-		Window replacement in Clarkes Estate, Phase 1.2 (Galedon, Elgin, Hazyview, Heathview courts)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids						
Sub level / Project	CPX.0017148-F1.WR.C2	ID No.10.22.2 Windows Replacement in Elsies River, Clarkes Estate Phase 1.2	1 563 555.28		Window replacement in Clarkes Estate, Phase 1.2 (Galedon, Elgin, Hazyview, Heathview courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor			4503735141	25 Aug 2020
Sub level / Project	CPX.0017148-F1.WR.C3	ID No.10.23.1 Windows Replacement in Elsies River, Clarkes Estate PH2.1	1 883 584.74		Window replacement in Clarkes Estate, phase 2.1 (Frere, Blanco, Luka, Marydale courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor			4503735142	25 Aug 2020
Sub level / Project	CPX.0017148-F1.WR.C4	ID No.10.23.2 Windows Replacement in Elsies River, Clarkes Estate PH2.2	1 699 958.81		Window replacement in Clarkes Estate, phase 2.2 (Martindale, Hibberdene, Holmdene & Glencor courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor			4503735140	25 Aug 2020
Sub level / Project	CPX.0017148-F1.WR.C5	ID No.10.24 Window Replacement in Elsies River, Clarkes Estate, Phase 3	544 230.28		Window replacement in Clarkes Estate (Glengarry Court)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13610416		4503739754	26 Aug 2020
Sub level / Project	CPX.0017148-F1.PS	Professional Services Phase 1	8 851 835.03		Professional Services Phase 1		Alistair Stanbull	Alistair Stanbull		PO released to vendor			4503734703	17 Aug 2020
Public Housing-Top Level/Programme	CPX.0017124-F1	Major Upgr Area Central - Ext Civil FY21	5 890 002.00		296Q (uitsig backyarder drainage upgrade) & 50Q (Civils term tender) available to spend budget. Re-phased from FY19/20 (ID6.1 & ID6.2 Stack relocations)		lan. Andre Davids	lan. Andre Davids						
Sub level / Project	CPX.0017148-F1.WR.C1	ID No.10.22.1 Windows Replacement in Elsies River, Clarkes Estate Phase 1.1	1 893 239.35		Window replacement in Clarkes Estate, Phase 1.1 (Heathview, Hawston, Howick Place and Hurlyvale courts)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		No movement on WBS				
Sub level / Project		ID No.10.22.1 Windows Replacement in Elsies River, Clarkes Estate Phase 1.1	-		Window replacement in Clarkes Estate, Phase 1.1 (Heathview, Hawston, Howick Place and Hurlyvale courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids						
Sub level / Project		ID No.10.21 Windows Replacement in Elsies River, Leonsdale 2	-		Window replacement in Leonsdale 1(De Doorns, De Hoek, Zeerust, Steyning, Groenkloof, Bereaville, Devondale and Alicedale Courts)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids						
Public Housing	-CPX.0017124-F1.SR	Sewer line replacement at cottages in Uitsig	2 316 519.16	2 316 519.16	Sewer line replacement at cottages in Uitsig. On property sewer lines to be relaid at cottages in Uitsig	Quetzal(296/2016/17) or AMS(50Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (budget cut) (rephased)					
Public Housing-Top Level/Programme	CPX.0017147-F1	Major Upgr Area Central - Ext Comp FY21	19 785 408.00		345Q/2018/19 Installation of windows and 243Q Re-phased projects from FY19/20 (ID4.1, ID4.3, ID10.14, ID10.15, ID10.16, ID10.17, ID10.18, ID10.19, ID4.2, ID10.20, ID10.22, ID10.21, ID10.23 & ID10.24 window replacement)		lan. Andre Davids	lan. Andre Davids						, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
Sub level / Project	CPX.0017147-F1.WR.WA	ID No.4.1 Windows Replacement in Adriaanse Phase 4a	1 115 276.45		Window replacement in Adriaanse Phase 4a (Napier, Oakdale, Orange Grove, Reitz and Petrusburg Court)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13607843		4503733729	21 Aug 2020
Sub level / Project	CPX.0017147-F1.WR.WB	ID No.4.1 Windows Replacement in Adriaanse Phase 4b	1 118 429.50		Window replacement in Adriaanse Phase 4b (Napier, Oakdale, Orange Grove, Reitz and Petrusburg Court)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13607844		4503733727	21 Aug 2020
Sub level / Project	CPX.0017147-F1.WR.WC	ID No.4.2 Window Replacement in Avonwood Phase 1A	1 020 474.09		Window Replacement in Avonwood Phase 1A	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13607842		4503733733	21 Aug 2020
Sub level / Project	CPX.0017147-F1.WR.WD	ID No.4.3.1 Window Replacement in Avonwood Phase 1B.1	1 333 508.56		Window replacement in Avonwood Phase 1B.1 (Orchard, Humewood Court)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor	13607841		4503733737	21 Aug 2020
Sub level / Project	CPX.0017147-F1.WR.WE	ID No.4.3.2 Window Replacement in Avonwood Phase 1B.2	1 390 492.77		Window replacement in Avonwood Phase 1B.2 (Heuningspruit and Hendrina Court)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13607840		4503733742	21 Aug 2020
Sub level / Project	CPX.0017148-F1.WR.L1	ID No.10.21 Windows Replacement in Elsies River, Leonsdale 1	-		Window replacement in Leonsdale 1(De Doorns, De Hoek, Zeerust, Steyning, Groenkloof, Bereaville, Devondale and Alicedale Courts)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids	Budget Moved to CPX.0017072-F1.					
Sub level / Project		ID No.10.21 Windows Replacement in Elsies River, Leonsdale 1	-		Window replacement in Leonsdale 1(De Dooms, De Hoek, Zeerust, Steyning, Groenkloof, Bereaville, Devondale and Alicedale Courts)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids						
Sub level / Project	CPX.0017147-F1.WR.WH	ID No.10.16 Windows Replacement in Elsies River, Adriaanse Phase 2.1a	1 183 254.01		Window replacement in Adriaanse Phase 2.1b (Koelen Hof, Kloof, Louisevale, Lineacres and Karin Court)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor	13607827		4503733759	26 Aug 2020

178

Sub level / Project	CPX.0017147-F1.WR.WI	ID No.10.16 Windows Replacement in Elsies River, Adriaanse Phase 2.1b	897 054.61	Window replacement in Adriaanse Phase 2.1a (Koelen Hof, Kloof, Louisevale, Lineacres	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to		4503737301	21 Aug 2020
Sub level / Project		ID No.10.17 Windows Replacement in Elsies River, Adriaanse Phase 2.2a	1 025 806.66	and Karin Court) Window replacement in Adriaanse, Phase 2.2a (Mayville, Montclair, Molteno and Nigel	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to	13607825	4503733762	21 Aug 2020
Sub level / Project		ID No.10.17 Windows Replacement in Elsies River, Adriaanse Phase 2.2b	1 126 240.53	Court) Window replacement in Adriaanse, Phase 2.2b (Mayville, Montclair, Molteno and Nigel	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to	13607826	4503733761	21 Aug 2020
-		ID No.10.18 Windows Replacement in Elsies River, Adriaanse Phase 3.1a	1 222 214.13	Court) Window replacement in Adriaanse, Phase 3.1a (Klawer, Northdene, Sanies, Sias and	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids		vendor PO released to	13607823	4503733764	20 Aug 2020
-				Rooiberg Courts) Window replacement in Adriaanse, Phase 3.1b (Klawer, Northdene, Sanies, Sias and					vendor PO released to	13607824		
Sub level / Project		ID No.10.18 Windows Replacemen in Elsies River, Adriaanse Phase 3.1b	796 461.87	Rooiberg Courts) Window replacement in Adriaanse, Phase 3.2 (Muldersdruf, Newclair, Newton Kloof,	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids		vendor PO released to		4503733763	21 Aug 2020
-		ID No.10.19 Windows Replacement in Elsies River, Adriaanse Phase 3.2	1 999 249.26	Northmead and Norwood Court)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		vendor PO released to	13607822	4503733766	21 Aug 2020
Sub level / Project		ID No.10.20.1 Windows Replacement in Elsies River , Avonwood Phase 2.1	1 681 257.35	Window replacement in Avonwood, Phase 2 (Bradfort, Blydoorn Court)	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		vendor		4503734757	21 Aug 2020
Sub level / Project		ID No.10.20,2 Windows Replacement in Elsies River , Avonwood Phase 2.2	-	Window replacement in Avonwood, Phase 2 (Abottsdale and Airlie Place Court) Window replacement in Adriaanse Phase 1.2 (Hectorspruit, Hermon, Kirkwood and	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids	"Budget exceeded" to be				
Sub level / Project	CPX.0017147-F1.WR.WG	ID No.10.15 Windows Replacement in Elsies River, Adriaanse Phase 1.2	1 812 197.66	Kingwood Court)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids	investigated by Sonia. WPD values are well within budget. "Budget exceeded" to be	Requisition created	13607839	Exceeded	
Sub level / Project	CPX.0017147-F1.WR.WF	ID No.10.14 Windows Replacement: in Elsies River, Adriaanse Phase 1.1	1 661 540.00	Window replacement in Adriaanse Phase 1.1 (Kassia, Kinross, Jacobsdal and Horison Court) Bellville Records Room -Hoheizen - The project scope accommodates the provision of	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids	investigated by Sonia. WPD values are well within budget.	Requisition created	13607838	Exceeded	
Sub level / Project		ID No. 8.1 Bellville - Records Room Hoheizen Depot	-	record management service infrastructure for the directorate Human Settlements. Building Work	TCC(243Q/2016/17)	Michael Lotter	Wayne Barends					
Public Housing	-CPX.0017086-F1.EP.LH	ID No12-External Paintwork in Lavender Hill Part 1	1 741 881.00	External paintwork to Deposition Cresent (30 blocks), Roos Court and Beulah Court	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem	Project Cancelled on 15.09.2020 (Rephased)	Project Cancelled			
Sub level / Project		ID No. 12 External Paintwork in Lavender Hill Part 1	-	External paintwork to Deposition Cresent (30 blocks), Roos Court and Beulah Court	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem					
Sub level / Project	-CPX.0017072-F1.NB	ID-No10.43 External Paintwork in Parkers Walk, Parkwood 2	1 115 516.00	External painting in Parkwood, Parkers Walk (17-blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem	Project Cancelled on 15.09.2020 (Rephased)	Project Cancelled			
Sub level / Project		ID No. 10.43 External Paintwork in Parkers Walk, Parkwood 2	-	External painting in Parkwood, Parkers Walk (17 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem					
Public Housing-Top Level/Programme	CPX.0017123-F1	Major Upgr Area Central - Ext Roof FY21	29 844 012.00	243Q/2016/17 Re-phased from FY19/20 (ID3.1, ID3.2, ID10.34, ID10.35, ID10.36, ID10.37, ID10.37, ID10.29, ID10.30, ID10.27, ID10.28 & ID10.26 Roof replacement projects)		lan. Andre Davids	lan. Andre Davids					
		Over Budget/Under Budget Sub Level Project Total	11.52 29 844 000.48									
Sub level / Project	CPX.0017123-F1.RP.RA	ID No.3.1 Roof replacement in Elsies River, Adriaanse Phase 4,1	1 084 189.95	Roof Replacement in Adriaanse Phase 4,1 (2 courts) building 7 and 8	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13606171	4503733806	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RB	ID No.3.1 Roof replacement in Elsies River, Adriaanse Phase 4,2	1 084 189.95	Roof Replacement in Adriaanse Phase 4,2 (2 courts) building 7 and 8	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor		4503737324	27 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RC	ID No.3.2 Roof replacement in Elsies River, Adriaanse Phase 5.1	1 084 189.95	Roof Replacement in Adriaanse, Phase 5.1 (2 courts) building 9 and 10	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor		4503731526	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RD	ID No.3.2 Roof replacement in Elsies River, Adriaanse Phase 5.2	1 084 189.95	Roof Replacement in Adriaanse, Phase 5.2 (2 courts) building 9 and 10	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13606168	4503733816	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RE	ID No.10.34 Roof replacement in Elsies River, Leonsdale Phase 1	1 987 446.94	Roof Replacement in Leonsdale, Phase 1 (2 courts) building 1 and 2	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids		PO released to vendor	13605128	4503735571	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RF	ID No.10.35 Roof replacement in Elsies River, Leonsdale Phase 2	1 987 447.00	Roof Replacement in Leonsdale, Phase 2 (2 courts) building 3 and 4	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13605077	4503735573	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RG	ID No.10.36 Roof replacement in Elsies River , Leonsdale Phase 3	1 987 446.94	Roof Replacement in Leonsdale, Phase 3 (2 courts) building 5 and 6	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13605129	4503735574	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RH	ID No.10.31 Roof replacement in Elsies River, Adriaanse Phase 3,1	1 063 433.00	Roof Replacement in Adriaanse, Phase 3,1 (2 courts) building 5 and 6	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13605130	4503735577	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RI	ID No.10.31 Roof replacement in Elsies River, Adriaanse Phase 3,2	1 063 500.85	Roof Replacement in Adriaanse, Phase 3,2 (2 courts) building 5 and 6	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13605131	4503735580	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RJ	ID No.10.37 Roof replacement in Elsies River, Leonsdale Phase 4	1 987 446.94	Roof Replacement in Leonsdale, Phase 4 (2 courts) building 7 and 8	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13605130	4503735577	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RK	ID No.10.38 Roof replacement in Elsies River, Leonsdale Phase 5	1 987 446.94	Roof Replacement in Leonsdale, Phase 5 (2 courts) building 9 and 10	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13605131	4503735580	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RL	ID No.10.29 Roof replacement in Elsies River, Adriaanse Phase 1,1	1 084 189.95	Roof Replacement in Adriaanse, Phase 1,1 (2 courts) Building 1 and 2	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor	13606117	4503733820	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RM	ID No.10.29 Roof replacement in Elsies River, Adriaanse Phase 1,2	1 084 189.95	Roof Replacement in Adriaanse, Phase 1,2 (2 courts) Building 1 and 2	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		PO released to vendor		4503731524	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RN	ID No.10.30 Roof replacement in Elsies River, Adriaanse Phase 2,1	1 084 189.95	Roof replacement in Adriaanse, Phase 2,1 (2 courts) building 3 and 4	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13606169	4503733813	27 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RO	ID No.10.30 Roof replacement in Elsies River, Adriaanse Phase 2,2	1 084 189.95	Roof replacement in Adriaanse, Phase 2,2 (2 courts) building 3 and 4	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13606170	4503733811	27 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RQ	ID No.10.27 Roof replacement in Elsies River, Clarkes Estate Phase 1	1 821 197.31	Roof Replacement in Clarkes Estate, Phase 1 (Gonubie court)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor		4503731527	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RS	ID No.10.28 Roof replacement in Elsies River, Clarkes Estate Phase 2	1 202 701.39	Roof Replacement in Clarkes Estate, Phase 2 (Hazyview Court)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids		PO released to vendor		440045070 4503731528	21 Aug 2020
Sub level / Project	CPX.0017123-F1.RP.RT	ID No.10.26 Roof replacement in Elsies River, Avonwood	1 104 625.00	Roof Replacement in Avonwood (1 Court)	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13605563	440045081 4503735570	21 Aug 2020
Sub level / Project	CPX.0017123-F1.EP	66Q/2017/18 Expansion	4 977 788.57	66Q/2017/18 Expansion		Alistair Stanbull	Alistair Stanbull					
Public Housing-Top Level/Programme	CPX.0017146-F1	Major Upgr Area Central - Ext Walls FY21	7 746 978.00	243Q/2016/17 or 345Q/2018/19. Re-phased from FY19/20 (ID10.40 & ID10.25)		Ian. Andre Davids	lan. Andre Davids					
		Over Budget/Under Budget	33 687.85	33 687.85								
		Sub Level Project Total							PO released to			
Sub level / Project	CPX.0017146-F1.EW.CA	ID No. 10.40 Langa Old Flats Hostels B, C, F & G	1 186 672.32	General building upgrades in Langa Old Flats, Block B, C, F and G	TCC(243Q/2016/17)	lan. Andre Davids	Ian. Andre Davids		vendor	13606346	4503733790	21 Aug 2020

Sub level / Project	CPX.0017146-F1.EW.CB	ID No. 10.25 External Painting in Uitsig Ph1	1 165 666.19	1 165 666.19	External Paintwork in Uitsig (18 courts) & Ravensmead (6 courts)	TCC(243Q/2016/17)	Ian. Andre Davids	lan. Andre Davids	Project cancelled (Budget cut (rephased)	PC-section (1906345	4503733764	21 Aug 2020
Sub-level / Project	CPX.0017146-F1.EW.CC	ID No. 10.25 External Painting in Uitsig Ph2	1 165 666.19	1 165 666.19	External Paintwork in Uitsig & Ravensmead	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (Budget cut (rephased)) PO measure in window	13856342	4503783787	21.44(.2020
Sub level / Project	CPX.0017146-F1.EW.CD	ID No. 10.25 External Painting in Ravensmead	768 892.47		External Paintwork in Ravensmead	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids		PO released to vendor	13606349	4503733780	21 Aug 2020
Sub level / Project	CPX.0017146-F1.RM.RA	ID No. 8.1 Bellville - Records Room Hoheizen Depot	1 812 378.78		Bellville Records Room -Hoheizen - The project scope accommodates the provision of record management service infrastructure for the directorate Human Settlements. Building Work	TCC(243Q/2016/17)	Michael Lotter	Wayne Barends		PO released to vendor	450373153	4503731532	21 Aug 2020
Sub level / Project	CPX.0017146-F1.RM.RB	ID No. 8.2 Beliville - Records Room Hoheizen Depot	1 614 014.20		Bellville Records Room -Hoheizen - The project scope accommodates the provision of record management service infrastructure for the directorate Human Settlements. HVAC/Elec Work	TCC(243Q/2016/17)	Michael Lotter	Wayne Barends		PO released to vendor	13605559	4503733829	21 Aug 2020
Public Housing-Top Level/Programme	CPX.0017125-F1	Major Upgr Area Central - Fencing FY21	1 000 000.00		50Q		lan. Andre Davids	Ian. Andre Davids					
		Over Budget/Under Budget	-										
		Sub Level Project Total	1 000 000.00		Waller and families in December 1				Desirate # 1 %	,			
Sub level / Project	CPX.0017125-F1.FA	Walling and fencing in Elsies River	1 000 000.00	1 000 000.00	Walling and fencing in Ravensmead, Avon, Clarke Estate, Adriaanse, Avonwood, Trinity- Place, Springbok Place	AMS (50Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (budget cut (rephased))-			
Public Housing-Top Level/Programme	CPX.0015782-F1	Major Upgr Area Central - Internal FY21	16 034 702.00		357Q/2018/19 (staircase term tender) to be cancelled and assumption that 66Q/2017/18 expansion to pilot double storey staircases will not be approved despite several double storey staircases collapsing, due to local office as elegibility criterion deemd bias by AGSA. budget to be spent aginst 296Q (Soil stack relocation including backyarder soil drainage upgrade to multi storeys in North & East Regions).		Zaahir Jassiem	Zaahir Jassiem					
Sub level / Project	CPX.0015782-F1.SR.SA	Soil stack relocation to multi storeys in North Area	1 397 134.72		7 Blocks in Heathfields, Atlantis (Phase 1)	Quetzal(296/2016/17)	Zaahir Jassiem	Zaahir Jassiem		PO released to vendor		4503728075	07 Aug 2020
Sub level / Project	CPX.0015782-F1.SR.SB	Soil stack relocation to multi storeys in North Area	392 310.00		2 Blocks in Heathfields, Atlantis (Phase 2)	Quetzal(296/2016/17)	Zaahir Jassiem	Zaahir Jassiem		PO released to vendor		4503743358	02 Sep 2020
Sub level / Project	CPX.0015782-F1.EP CPX.0015782-F1.RR.RA	66Q/2017/18 Expansion Asbestos Roof Replacement - Macassar Block H6	10 923 947.51 482 465.94		66Q/2017/18 Expansion Macassar Block H6	TCC(243C)2046(47)	Alistair Stanbull Tivani Hlongwane	Alistair Stanbull Tivani Hlongwane		Status unknown PO released to		4503734143	17 Aug 2020
Sub level / Project	CPX.0015/82-F1.RR.RA CPX.0017086-F1.EP.PW	Asbestos Koof Replacement - Macassar Block H6 ID No. 10.43 External Paintwork in Parkers Walk Parkwood 1	482 465.94 1 392 064.00		Macassar Block H6 External painting in Parkwood, Parkers Walk (17 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem	Project Cancelled on-	vendor		4503734143	11 Aug 2020
Public Housing Public Housing-Top		,				1CC(243Q/2016/17)			15.09.2020 (Rephased)	Project Cancelled			
Level/Programme	CPX.0017069-F1	Major Upgr Area East - External (Roofing) OverBudget/Under Budget	416 000.00		243Q		Tivani Hlongwane	Tivani Hlongwane					
Sub level / Project	CPX.0017069-F1.AR	Sub Level Project Total Asbestos Roof Replacement -Macassar	416 000.00 416 000.00		Macassar Block F2 Roofing and Ceilings	TCC(243Q/2016/17)	Tivani Hlongwane	Tivani Hlongwane		PO released to vendor		4503727266	03 Aug 2020
Public Housing-Top Level/Programme	CPX.0017066-F1	Major Upgr Area East - External (Walls)	418 000.00		243Q		Tivani Hlongwane	Tivani Hlongwane					
		OverBudget/Under Budget Sub Level Project Total	- 418 000.00										
Sub level / Project	CPX.0017066-F1.MR	Asbestos Roof Replacement - Macassar	418 000.00		Macassar Block F3 Roofing and Ceilings	TCC(243Q/2016/17)	Tivani Hlongwane	Tivani Hlongwane		PO released to vendor		4503727265	03 Aug 2020
Public Housing-Top Level/Programme	CPX.0017071-F1	Major Upgr Area North - External (Roofin	2 027 498.00		243Q		Zaahir Jassiem	Zaahir Jassiem					
		Over Budget/Under Budget Sub Level Project Total	448 525.00 1 578 973.00										
Sub level / Project	CPX.0017071-F1.AT	Asbestos Roof Replacements -Atlantis	1 578 973.00		Atlantis Roof Replacements Blocks Oyster Place 35-46, Shelly Crt	TCC(243Q/2016/17)	Zaahir Jassiem	Zaahir Jassiem		PO released to vendor		4503739983	28 Aug 2020
Sub level / Project		ID No. 10.43 External Paintwork in Parkers Walk, Parkwood 1	-		External painting in Parkwood, Parkers Walk (17 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem					
Public Housing-Top Level/Programme	CPX.0017068-F1	Major Upgr Area North - External (Walls)	2 000 000.00		243Q		Zaahir Jassiem	Zaahir Jassiem					
Sub level / Project	CPX.0017068-F1.AF	Atlantis Façade Upgrade	2 000 000.00		Atlantis balance of Island Place 4 Blocks	TCC(243Q/2016/17)	Zaahir Jassiem	Zaahir Jassiem		PO released to		4503740684	27 Aug 2020
Public Housing-Top Level/Programme	CPX.0017072-F1	Major Upgr Area North - Services (Electr	5 000 000.00		212Q, 128Q & 308Q (ELECTRICAL WORKS TERM TENDERS) are available to spend budget. Obtain increase from CPX.0015782-F1 as 357Q/2018/19 (staircase term tender) to be cancelled due to local office as elegibility criterion deemd bias by AGSA.		Zaahir Jassiem	Zaahir Jassiem	Await Goolam to finalise budget reduction post virement. Do not touch this budget.	vendor			
Sub level / Project	CPX.0017072-F1.NA	Electrical Upgrade - Atlantis	538 133.00		Upgrade rental units in Area 1 by rewiring entire buildings - Atlantis Blocks TBC	212Q/2016/17 or 286Q/2018/19	Zaahir Jassiem	Zaahir Jassiem	Project packaging in progress Delta BEC	3 -			
Sub level / Project	CPX.0017019-F1.WR.WB	ID No. 10.2 Window Replacement in Grassy Park(Jade, Marmer, Opal, Diamond,	1 188 031.29		Window replacement in Grassy Park (Jade, Marmer, Opal, Diamond, Emerald)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem	Project Cancelled on	Project Cancelled			
Sub level / Project		Emeraid) ID No.10.21 Windows Replacement in Elsies River, Leonsdale 1	1 416 132.00		Window replacement in Leonsdale 1(De Dooms, De Hoek, Zeerust, Steyning,	TCC(243Q/2016/17)	Ian. Andre Davids	Ian. Andre Davids	15.09.2020 (Rephased)	PO released to		4503736356	21 Aug 2020
Public Housing-Top	CPX.0017072-F1.WR.L1	Major Upgr Area South - External (Roofin			Groenkloof, Bereaville, Devondale and Alicedale Courts)	.00(2-100/2010/11)				vendor		.550700000	2.7.ug 2020
Level/Programme	O. A.0017022-F1	Wajor Upgr Area South - External (Room) Over Budget/Under Budget	- 13 233 642.00 - 2.01		243Q Re-phased projects from FY20/21 (ID10.6 & ID10.8)		Terence Bent	Zaahir Jassiem					
		Sub Level Project Total											
Sub level / Project	CPX.0017022-F1.RP.LA	ID No. 10.6 Roof Replacement & External Paintwork in Lavender Hill Part 2	1 422 578.97		Roof Replacement & External Paintwork in Lavender Hill Part 2 (Beulah Court building 1)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503725916	07 Aug 2020
Sub level / Project	CPX.0017022-F1.RP.LB	ID No. 10.8 Roof Replacement & External Paintwork in Lavender Hill Part 3	1 224 208.14		Roof Replacement & External Paintwork in Lavender Hill Part 2 (Beulah Court building 2)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718414	19 Jul 2020
Sub level / Project	Requires Sub Level WBS	66Q/2017/18 Expansion	10 586 856.90		66Q/2017/18 Expansion		Alistair Stanbull	Alistair Stanbull					
Public Housing-Top Level/Programme	CPX.0017019-F1	Major Upgr Area South - External (Walls)	13 233 642.00		243Q. Re-phased projects from FY20/21 (ID 10.1, ID10.4, ID10.9, ID10.10, ID10.11, ID10.13, ID10.12, ID10.1 & ID10.43)		Terence Bent	Zaahir Jassiem					
Sub level / Project	CPX.0017019-F1.WR.WA	ID No. 10.1 Window Replacement in Grassy Park (Slate, Pearl, Garnet, Robyn)	1 159 930.79		Window replacement in Grassy Park (Slate, Pearl, Garnet, Robyn Court)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem	Project Cancelled on 15.09.2020 (Rephased)	Project Cancelled			
Sub-level / Project	CPX.0017124-F1.SP.R3	ID 6.2 Stack Pipe Replacement in Uitsig Phase 2	1 133 510.58	1 133 510.58	Stack Pipe Replacement in Uitsig Phase 2 (5 courts)	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (Budget cut (rephased)	PO creates real		4503733794	
Sub level / Project	CPX.0017019-F1.WR.WC	ID No. 10.4.1 Window Replacement and External Paintwork in Ocean View Phase 2.1	1 149 414.57		Window Replacement and External Paintwork in Ocean View Phase 2.1, MILKY WAY (2	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to		4503725912	07 Aug 2020
Sub level / Project		ID No. 10.4.2 Window Replacement and External Paintwork in Ocean View Phase 2.2	1 149 414.57		Blocks) Window Replacement and External Paintwork in Ocean View Phase 2.2, MILKY WAY Blocks (2 Blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor	13593035	4503732512	21 Aug 2020
Sub level / Project	CPX 0017019-F1 WR WE	ID No. 10.4.3 Window Replacement and External Paintwork in Ocean View Phase 1.1	1 149 414.57		Window Replacement and External Paintwork in Ocean View Phase 1.1, Blocks (MILKY	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to		4503725915	07 Aug 2020
Sub-level / Filoject	O. A.OO I O 15-1 1.WK.WE	10. 10. THROW REPRODUCTION OF THE PROPERTY OF	1 145 414.5/		WAY 2 Blocks)	100(2400/2010/17)	. Sicilos Belli	_can iii oassiciii		vendor		.000120010	5 lug 2020

Sub level / Project	CPX.0017019-F1.WR.WF	ID No. 10.4.4 Window Replacement and External Paintwork in Ocean View Phase 1.2	1 149 414.57		Window Replacement and External Paintwork in Ocean View Phase 1.1, Blocks (MILKY WAY 2 Blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503725914	07 Aug 2020
Sub level / Project	CPX.0017019-F1.WR.WG	ID No. 10.9 External Paintwork in Parkwood, Willow Walk	728 840.13		External Paintwork in Parkwood, Willow Walk	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718419	18 Jul 2020
Sub level / Project	CPX.0017019-F1.WR.WH	ID No. 10.10 Window Replacement and servicing in Parkwood, Willow & Parkers Walk	1 532 952.67		Window replacement & servicing in Parkwood, Willow Walk (16 Blocks) and Parkers Walk (17 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718425	19 Jul 2020
Sub level / Project	CPX.0017019-F1.WR.WI	ID No. 10.11 External painting in Retreat, Joe Marks Avenue	883 863.47		External paintwork in Retreat, Joe Marks Avenue (28 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718424	18 Jul 2020
Sub level / Project	CPX.0017019-F1.WR.WJ	ID No. 10.13 Window replacement in Retreat, Joe Marks Avenue (15-28 blocks)	1 153 262.19		Window replacement in Retreat, Joe Marks Avenue (15-28 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718407	19 Jul 2020
Sub level / Project	CPX.0017019-F1.WR.WK	ID No. 10.12 Window replacement in Retreat, Joe Marks Avenue	1 153 262.19		Window replacement in Retreat, Joe Marks Avenue (1-14 blocks)	TCC(243Q/2016/17)	Terence Bent	Zaahir Jassiem		PO released to vendor		4503718411	19 Jul 2020
Sub level / Project	CPX.0017124-F1.SP.R2	ID 6.1 Stack Pipe Replacement in Uitsig Phase 1.2 (10 Courts)	1 219 986.63	1 219 986.63	Stack Pipe Replacement in Uitsig Phase 1.2 (10 Courts)	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (Budget cut) PO created (not-	13635341	4503730150	
Sub level / Project	CPX.0017124-F1.SP.R1	ID 6.1 Stack Pipe Replacement in Uitsig Phase 1.1 (10 Courts)	1 219 985.63	1 219 985.63	Stack Pipe Replacement in Uitsig Phase 1.1 (10 Courts)	TCC(243Q/2016/17)	lan. Andre Davids	lan. Andre Davids	Project cancelled (Budget cut) No mevement on			
Sub level / Project	CPX.0017071-F1.SC	Asbestos Roof Replacements -Scottsdene	448 525.00		Scottsdene Roof & Ceiling Replacements Rivonia Court 1 block	TCC(243Q/2016/17)	Zaahir Jassiem	Zaahir Jassiem	(topnasou)	PO released to		4503741293	02 Sep 2020
Public Housing-Top Level/Programme	CPX.0015783-F1	Major Upgr Area South - Internal FY21	11 633 253.00		357Q/2018/19 (staircase term tender) to be cancelled and assumption that 66Q/2017/18 expansion to pilot double storey staircases will not be approved despite several double storey staircases collapsing, due to local office as elegibility criterion deemd bias by AGSA. budget to be spent aginst 296Q (Soil stack reolcation including backyarder soil drainage upgrade to multi storeys in South Region) and 212Q, 128Q & 308Q (ELECTRICAL WORKS TERM TENDERS) are available to spend budget.		Terence Bent	Zaahir Jassiem		versuoi			
		Over Budget/Under Budget	7 633 253.00	7 633 253.00									
		Sub Level Project Total	4 000 000.00										
Sub level / Project	sub-level WBS required	66Q/2017/18 contingency softlock	4 377 871.00		66Q/2017/18 contingency softlock	GHC 66Q/2017/18	Alistair Stanbull	Alistair Stanbull		Status unknown			
Sub level / Project	CPX.0015783-F1.SA	Soil stack reolcation in Ocean View phase 1	2 000 000.00		Ocean View	Quetzal(296/2016/17)	Terence Bent	Zaahir Jassiem		Status unknown			
Sub level / Project	CPX.0015783-F1.SB	Soil stack reolcation in Ocean View phase 2	2 000 000.00		Ocean View -Water	Quetzal(296/2016/17)	Terence Bent	Zaahir Jassiem		Status unknown			
Public Housing	CPX.0017024-F1	Trunking Radios: Additional FY21	550 000.00		Trunking radios purchased over a 12 month period as and when required.	RFQ	Portia September	Sonia Fillies		PO released to vendor	13609329	4503742714	02 Sep 2020
Public Housing	CPX.0017149-F1	Upgrading of Depots - Central FY21	500 000.00		Upgrading of Depots in Central region. Upgrade of Bishop Lavis -Carpeting & vinyl floor covering; new airconditioners, partitioning construction of boardroom		lan. Andre Davids	lan. Andre Davids					
		Over Budget/Under Budget											
		Sub Level Project Total								PO released to			
Sub level / Project	CPX.0017149-F1.CA	Upgrading of Depots Central	500 000.00			Aveng Grinaker (29Q/2016/17	lan. Andre Davids	Ian. Andre Davids		vendor		4503727779	03 Aug 2020
Sub level / Project		Upgrading of Depot Store - Central	-		Upgrading of Depot Store - Central	Various	Portia September	Portia September					
Public Housing	CPX.0017073-F1	Upgrading of Depots - East FY21	481 041.00		Zaahir to provide detailed scope		Tivani Hlongwane	Tivani Hlongwane					
		Over Budget/Under Budget	231 041.00	231 041.00									
Sub level / Project	CPX.0017073-F1.EA	Sub Level Project Total				Taskinda assaida	ThereitHeather	The still of the s	TH - Because of the budget				
	CFX.001/0/3-F1.EA	Upgrading of Depots East	250 000.00			Zaahir to provide	Tivani Hlongwane	Tivani Hlongwane	shortfall,we are revising the scope of work	Waiting for new quotes.			
Sub level / Project		Upgrading of Depot Store - East	-		Upgrading of Depot Store - East	Various	Portia September	Portia September					
Public Housing	CPX.0017075-F1	Upgrading of Depots - North FY21	250 000.00		Zaahir to provide detailed scope		Zaahir Jassiem	Zaahir Jassiem					
		Over Budget/Under Budget Sub Level Project Total											
Sub level / Project	CPX.0017075-F1.NA	Upgrading of Depots North	250 000.00	250 000.00		Aquila (254G/2016/17)	Zaahir Jassiem	Zaahir Jassiem					
Sub level / Project		Upgrading of Depot Store - North	-		Upgrading of Depot Store - North	Various	Portia September	Portia September	Project cancelled (budget cut) (rephased)	+			
Public Housing	CPX.0017023-F1	Upgrading of Depots - South FY21	250 000.00		Aiming to gain additional funding - Terence liaising with Contractors. Sites to be confirmed in Grassy Park		Terence Bent	Zaahir Jassiem	(горгазов)				
		Over Budget/Under Budget	-										
	ODV 0045	Sub Level Project Total				_	_						
Sub level / Project	CPX.0017073-F1.SA	Upgrading of Depots South	250 000.00			Terence to Provide	Terence Bent	Zaahir Jassiem		Status unknown			
Sub level / Project		Upgrading of Depot Store - South	-		Upgrading of Depot Store - South	Various	Portia September	Portia September					
Public Housing Top Level/Programme	CPX.0013568-F1	Install Rental Stock Sub-Meters FY21	9 307 651.00		Budget transferred from FY19/20 to complete projects not completed due to COVID-19 delays. Tenders: 415/2016/17, \$3Q/2016/17 & 197Q/2018/19. Projects are (Leonsdale (Type 1 & 2) (352 units, 25 buildings, Avon Estate (192 units, 12 buildings), Ocean View (600 units, 48 buildings), Lavender Hill Staircase Reinstatement (288 units, 12 buildings), Lotus River B WP6 (9 buildings), Lotus River C-F WP7 (9 buildings), Grassy Park WP8 (6 buildings), Plumstead A (2.5 buildings), WP10A Targeted Labour, WP10 B Targeted CLO, WP10C Emergency Repairs at Ottery, Ottery B WP3B, Ottery B WP3C, Ottery B WP4B, Ottery B WP3A & Solum Flats Geysers. Available term tenders do not contain pertenant rates to execute scope in rental stock, eg. Local labour & Community Liason Officer, as these rates are critical for the success of projects in rental stock. Secondly, 356Q/2018/19 (general building term tender) to be cancelled due to local office as elegibility criterion deemd bias by AGSA.		Alistair Stanbull	Alistair Stanbull	Await Goolam to finalise budget reduction post virement. Do not touch this budget.				
		Over Budget/Under Budget	4 881 881.98	4 131 882.00									
		Sub Level Project Total	4 425 769.02										
Sub level Project	CPX.0013568-F1.RS.RA	WP7 External water supply riser installation in Lotus River C to F	90 565.87		External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Lotus River C to F (9 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull		PO released to vendor		4503726633	28 Aug 2020
Sub level Project	CPX.0013568-F1.RS.RC	WP3A External water supply riser installation in Ottery B	932 776.66		External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Ottery B (7 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull		PO released to vendor		4503726636	28 Aug 2020

Level/Programme	CPX.0013023-F1	Records Management IT System	4 051 330.00	EG Parkwood housing, Macassar and Gugulethu. The Director then decided that we explore a place of safe keeping for all files as Ndabeni is to small, it was approved that Hoheizen be the records room store requiring upgrade.		Michael Lotter	Wayne Barends			
Public Housing Top				Top level budget committed to consultant fees for, Scanning and Change agent. This was mainly to protect the files from being destroyed due to protest action for						
Sub level Project	CPX.0013568-F1.MW.MB	WP14 CLOs	369 488.79	Community Liaison Officers (CLOs) for for WP3 and WP4	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503727486	28 Aug 2020
Sub level Project	CPX.0013568-F1.MW.MA	WP13 Local Labour	785 906.55	Targeted labour for WP3 and WP4	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503727484	28 Aug 2020
Sub level Project	CPX.0013568-F1.RS.RG	WP4B External water supply riser installation in Ottery B	218 764.09	External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Ottery B (4 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503726634	28 Aug 2020
Sub level Project	CPX.0013568-F1.RS.RF	WP4A External water supply riser installation in Ottery B	226 816.59	External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Ottery B (3 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503726635	28 Aug 2020
Sub level Project	CPX.0013568-F1.RS.RE	WP3C External water supply riser installation in Ottery B	929 375.54	External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Ottery B (4 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503733261	28 Aug 2020
Sub level Project	CPX.0013568-F1.RS.RD	WP3B External water supply riser installation in Ottery B	872 074.93	External water underground ring main installations connecting metered external municipal supply to sub-metered manifolds for Ottery B (7 buildings)	Nejeni (53Q/2016/2017)	Alistair Stanbull	Alistair Stanbull	PO released to vendor	4503726674	28 Aug 2020
